

**BEFORE THE NATIONAL GREEN TRIBUNAL  
PRINCIPAL BENCH, NEW DELHI**  
Original Application No. 6/2012 (IA No. 72/2024 & IA No. 276/2024)  
WITH  
Execution Application No. 5/2024  
IN  
Original Application No. 6/2012

**IN THE MATTER OF:**

**NIZAMUDDINWESTASSOCIATION (REGD.) ..... APPLICANT**

**VERSUS**

**UNIONOFINDIA & ORS.**

**... RESPONDENTS**

**INDEX**

<b>Sl No.</b>	<b>Particulars</b>	<b>PG.No.</b>
1.	Affidavit	1-2
2.	<b><u>ANNEXURE-I</u></b> True copy of present status of STPs/DSTPs	3-4
3.	<b><u>ANNEXURE-II</u></b> True copy of list of JJC clusters	5-14
4.	<b><u>ANNEXURE-III</u></b> True copy of list 40 new DSTPs	15-16
5.	<b><u>ANNEXURE-IV</u></b> True copy of status report of water quality of untapped outfalling drains into Yamuna (Jan., 2023 & Jan., 2024)	17-20
6.	<b><u>ANNEXURE-V</u></b> True copy of list of trapped drains	21-28

Through



Sh. Bhupesh Kumar  
Chief Engineer  
DELHI JAL BOARD

New Delhi  
Date:01.08.2024

**BEFORE THE NATIONAL GREEN TRIBUNAL  
PRINCIPAL BENCH, NEW DELHI**

Original Application No. 6/2012 (IA No. 72/2024 & IA No. 276/2024)

WITH

Execution Application No. 5/2024

IN

Original Application No. 6/2012

**IN THE MATTER OF:**

**NIZAMUDDIN WEST ASSOCIATION (REGD.) ..... APPLICANT**

**VERSUS**


**UNION OF INDIA & ORS.**

**... RESPONDENTS**


**AFFIDAVIT**

I, Bhupesh Kumar, S/o Sh. R.P. Bhaskar, aged about 55 Yrs, designated as Chief Engineer Drainage Project, Delhi Jal Board, at Govt. of N.C.T. of Delhi Jhandewalan, karolbagh New Delhi-110005, solemnly affirm and sincerely state as follows:

1. That Applicant namely Nizamuddin West Association (Registered) through its president seeks execution of the Order dated 13.01.2015 passed by this Hon'ble Tribunal in O.A. No. 6 of 2012 in the present Execution Application No. 5/2024. Simultaneously, the Applicant has also preferred I.A. No. 170 of 2024 seeking certain directions for taking adequate remedial measures for removal of pollution from the Barapullah Drain in Delhi which is now listed on 02.08.2024.
2. That vide order dated 04.07.2024, the Hon'ble Tribunal directed DDA, Govt. of NCT Delhi, DJB and MCD to place on record in the form of affidavit the documents which were handed over to the Hon'ble Tribunal on the day of hearing i.e. 04.07.2024.




3. That since, the matter is of utmost importance. The following documents are enclosed along for the kind perusal of this Hon'ble Court in compliance to order dated 04.07.2024:-
- i. Updated status of STPs/DSTPs by DJB followed to the major decisions taken by High Level Committee (HLC) is attached herein as **ANNEXURE-I**.
  - ii. Updated status and details of JJC Clusters is attached as **ANNEXURE-II**.
  - iii. Updated status and list of 40 new DSTPs is attached as **ANNEXURE-III**.
  - iv. Updated status of water quality of Yamuna and untapped drains falling into Yamuna River between Jan. 2023 & Jan. 2024 is attached as **ANNEXURE-IV**.
  - v. Updated status and list of trapped drains is attached as **ANNEXURE-V**.
4. I state that the contents of the aforesaid documents enclosed along with this affidavit are true and correct and duly verified by the undersigned and have been supplied by me to the counsel to be annexed herewith.
5. I further state that Delhi Jal Board shall remain duty bound by any direction or order by this Hon'ble Tribunal as and when directed.


  
**DEPONENT**

**VERIFICATION**

Verified at New Delhi on this 01 day of August, 2024 that the contents of the above affidavit are true and correct to my knowledge and as derived from the record maintained by Delhi Jal Board and nothing material has been concealed therefrom.



01 AUG 2024

  
**DEPONENT**

**ATTESTED**  
**NOTARY PUBLIC DELHI**  
 Govt. of India  
 Mob.: 9654768498

**Sub: Monthly Action Taken Report (June-2024) for submission to Hon'ble High Court w.r.t. 08.04.2024 in W.P(C) 7594/2018.**

Action Taken Report for S.No. 3(a) & 3(b) is as under:

SN	Name of STP	Present Sewage Treatment Capacity (MGD)	Standard Designed Parameters for treated sewage water	Capacity under augmentation (MGD)	Capacity under upgradation (MGD)	Status/ATR as on 30.06.2024
1	Okhla STP Ph-VI	30	10/10	0	0	-
2	Delhi Gate Phase II	15	10/10	0	0	-
3	Delhi Gate Phase I	2.2	10/15	0	0	-
4	SNH Nallah STP	2.2	10/15	0	0	-
5	Chilla	9	10/10	0	0	-
6	Akshardham CWG	1	2/1	0	0	-
7	New Coronation Pillar	70	10/10	0	0	-
8	Nilothi Phase-II	20	10/10	0	0	-
9	Pappankalan-II	20	10/10	0	0	-
10	Kapashera	5	10/10	0	0	-
11	Kondli STP Phase I	10	10/10	0	0	Kondli Ph-I, II & III have been upgraded recently under YAP-III and under trial run.
12	Kondli Ph-II	25	10/10	0	0	
13	Kondli STP Phase III	10	10/10	0	0	
14	Rithala-II	40	10/10	0	0	Upgradation done on 31.10.23
15	Rithala Ph-I	40	10/10	0	0	Upgradation work for achieving 10/10 under trial and likely to be completed by Sept 2024.
16	Kondli STP Phase IV	45	10/10	0	0	Upgradation work for achieving 10/10 is completed and the plant is under trial run.
17	Yamuna Vihar Phase II	15	10/10	0	0	Upgradation work for achieving 10/10 is completed and the plant is under trial run.
<b>Total</b>		<b>359.4</b>				
18	Okhla STP Ph-II	12	30/50	30	124	DJB is constructing a new 124 MGD plant at Okhla. The liquid stream is commissioned recently and under trail run treating 50MGD sewage. Once the new plant is stabilized the existing Okhla STP Ph-II, III & IV shall be closed.
19	Okhla STP Ph-III	37	30/50			
20	Okhla STP Ph-IV	45	30/50			
21	Nilothi Phase-I	40	30/50	20	60	Upgradation /augmentation of half stream is in progress.
22	Pappankalan-I	20	30/50	10	30	All electrical /mechanical equipment of half stream have been received. Maximum incoming raw sewage is being treated as on date. Overall physical progress of STPs is about 43% and financial progress is only 30%.

*Heer*

23	Keshopur-II	20	30/50	0	20	<p>Half stream has been upgraded /augmented to BOD/TSS &lt; 10/10 mg/l and under trial run.</p> <p>All major electrical /mechanical equipment have been received at site.</p> <p>Civil work for remaining half stream i/c tertiary units is in progress. Maximum incoming raw sewage is being treated as on date. Overall physical progress of STPs is about 67% and financial progress is only 37%.</p>
24	Keshopur-III	40	30/50	20	60	
25	Najafgarh	5	30/50	0	5	
26	Coronation Pillar Ph-II	20	30/50	0	20	
27	Coronation Pillar Ph-III	10	30/50	0	10	<p>Half stream has been upgraded /augmented to BOD/TSS &lt; 10/10 mg/l and under trial run.</p> <p>100% incoming raw sewage is being treated as on date.</p>
28	Narela STP	10	30/50	5	15	
29	Rohini Sec. 25	15	30/50	10	25	<p>All major electrical /mechanical equipment have been received at site.</p> <p>Civil work for remaining half stream i/c tertiary units is in progress. Overall physical progress of STPs is about 69% and financial progress is only 52%.</p>
30	Yamuna Vihar Phase I	10	30/50	5	15	<p>The block estimate is under process for in principle approval.</p>
31	Yamuna Vihar Phase III	25	20/30	30	55	
32	Okhla STP Ph-V	16	30/50	0	16	<p>The tender was invited and rejected due to a single bid the proposal is under the process for re-invitation</p>
33	Mehrauli STP	5	20/30	2.5	7.5	
34	Vasant Kunj Old	5	30/50	2.5	7.5	
35	Vasant Kunj New		30/50			
36	Ghitorni	5	30/50	2.5	7.5	
37	Molar band	0.66	30/50	0	0.66	<p>The block estimate is under process for in principle approval.</p>
38	Keshopur-I	12	20/30	6	18	<p>The tender was invited and rejected due to a single bid the proposal is under the process for re-invitation</p>
39	Sonia Vihar	0	10/10	0	7	<p>The liquid line of the plant shall be commissioned by July, 2024</p>
40	Delhi Gate Phase III	0	0	0	10	<p>Land is yet to be handed over by L&amp;DO, MoUHA to DJB.</p> <p>The work will be completed in 12 months after award of work.</p>
<b>Total (MGD)</b>		<b>712</b>		<b>143.5</b>	<b>513.16</b>	

**Note:**

1. 17 Nos. of STPs are working on 10/10 having capacity of **359.4 MGD**
2. 23Nos. of STPs are being upgraded/new constructed on 10/10 having capacity of **513.16 MGD**
3. 40 Nos. of DSTPs having capacity of 92 MGD are to be constructed.

**Total Capacity: 964.56 MGD.**

  
 EO to CE(SDW)

10776

**Status of trapping of JJC drains as on 20.07.2024**

<b>S. No.</b>	<b>Measures proposed by DJB/ Status</b>	<b>No. of JJ Clusters</b>
1	Trapped	1
2	Drains to be trapped in sewer line (work in progress) of nearby area	12
3	Drains will be trapped after commissioning of proposed sewer network in nearby U/A col.	14
4	Drains which can be trapped in to sewerage network by installing lift station	5
5	Feasible sites approved by NMCG for which demand has been raised for funds from NMCG	15
6	Trapped in STP through major storm water drain/trapping work are in progress	8
7	Not feasible due to space constraints and multiple outfalls etc.	3
8	Site does not exist.	1
	<b>Total</b>	<b>59</b>

**List of 59 JJ Clusters with Status and Timelines for connecting with Sewerage System/DSTPs**

10778

S.No. of 59 JJC list	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer ( Chief Engineer )	Name of SE	Name of EE and Division	Present status
1	Dr.Ambedker JJC Near Wazirabad Timarpur.	30.09.2024	Sh. Gajendra Tomar, CE(Central-North)	Sh Pawan Kumar, SE(M)-4	Sh Maninder Jeet Singh, EE(M)-03	Work order issued for installation of DSTP.
2	Okhla DTC Depot-I	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh. Naresh Kumar EE(M)-51	There is some public hindrance however, the drain will be trapped by Dec 2024
3	Gandhi Camp Behind Fruit & Vegetable Market Okhla Railway Station	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh. Naresh Kumar EE(M)-51	There is some public hindrance however, the drain will be trapped by Dec 2024
4	Khub Ram park Pem Nagar Kirari	31.12.2024	Sh. Gajendra Tomar, CE(West )	Sh B.S Rawat, SE(M)-7/ Sh. Ajay Kumar, SE(C)-6	Sh Harish Chander, EE(M)-9 / Sh. N.K.Sharma, EE(Pr)Sr.-I	The work of laying the sewer line in Kirari GoC is in progress and this drain will be trapped into sewer line by 31.12.2024 by Maintenance Wing.
5	Madrasi Basti Near Railway Line Jal Vihar	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh N.K Verma, EE(M)-41	Installation of DSTP not feasible due to jhuggies are present both side of railway track and forming multiple discharge points, space is also not available. However, this drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.
6	Shri Ram JJC near SPRINGDALE School Dhaula Kaun	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	Installation of DSTP is not feasible due to space constraints. However, this drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.
7	Ambedkar Basti West Block-II R.K.Puram	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	Installation of DSTP is not feasible, as discharge into storm water drain is directly from individual household. Discharge pipes from individuals houses are underground upto the storm water drain.Hence, it is difficult to collect discharge of JJC at single point. However, this drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.
8	Leprosy Colony Infront of Mohan Singh Market R.K.Puram	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	Installation of DSTP is not feasible, as discharge into storm water drain is directly from individual household. Discharge pipes from individuals houses are underground upto the storm water drain.Hence, it is difficult to collect discharge of JJC at single point. However, this drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.
9	Nehru Ekta Camp Sector-VII R.K.Puram	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	This drain will be trapped into DJB sewerage network by Maintenance Wing by 31.12.2024.
10	S.P./J.P. Colony Sector 6 R.K.Puram	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	This drain will be trapped into DJB sewerage network by Maintenance Wing by 31.12.2024
11	Sector-I R.K.Puram Police Post (Hanuman Camp)	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	Installation of DSTP is not feasible due to space constraints. However, this drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.

10779

S.No. of JJ Cluster	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer ( Chief Engineer )	Name of SE	Name of EE and Division	Present status
12	Ravi Dass Camp Sector-3 R.K.Puram	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
13	Nepali Camp Near Bhanwar Singh Camp Vasant Vihar	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	This drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.
14	Bhanwar Singh Camp Behind Janta Flat Block-D Vasant Vihar Phase-I	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	This JJC will be trapped by maintenance wing into sewer network by installing lift station and laying sewer line. NMCG team has also suggested the same during joint inspection.
15	Sewa Camp Behind Police Staff Quarter Vasant Vihar Depot Munirika	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	Installation of DSTP is not feasible due to space constraints. However, this drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.
16	Shiva Camp Vasant Vihar Near Petrol Pump	The discharge from the JJC drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Sanjay Jain, EE(M)-44	Installation of DSTP is not feasible as discharge into storm water drain is directly from individual household. Discharge pipes from individuals houses are underground upto the storm water drain.Hence, it is difficult to collect discharge of JJC at single point. However, this drain is ultimately out-falling in Barapulla Drain which is likely to be trapped by 30.09.2024.
17	Jagdamba Camp Near SFS Sheikh Sarai	The sewage discharge of jagdamba camp is falling into Chirag Delhi Drain which is ultimately trapped at krishi vihar hence there is no need of trapping at this point.	Sh. Gajendra Tomar, CE(South)	Sh S K Dahiya, SE(M)-10	Sh S C Jain, EE(M)-50	<b>Trapped</b>

S.No. of 59 JJC list	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer ( Chief Engineer )	Name of SE	Name of EE and Division	Present status
18	Priyanka Camp Mathura Road Opposite Sukhdev Vihar Depot	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Naresh Kumar, EE(M)-51	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
19	CRRRI Camp Mathura Road Opposite Sukhdev Vihar Depot	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya SE(M)-10	Sh Naresh Kumar, EE(M)-51	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
20	Priya Camp Mathura Road Opposite Sukhdev Vihar Depot	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh S.K.Dahiya ACE(M)-10	Sh Naresh Kumar, EE(M)-51	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
21	Shahbad Daulatpur Block-A, E & F	31.07.2024	Sh. Gajendra Tomar, CE(Central-North)	Sh. Sukhpal Chauhan, SE (M)-3 / Sh. Anil Kumar, SE(C)-5	Sh Sandeep Sharma, EE(M)-7 / Sh. Ashish Kumar, EE(C)DR-III	The work of laying the sewer line in Shahbad GoC is in progress and this drain will be trapped into sewer line by 31.07.2024 by Maintenance Wing.
22	Jhuggies Kholi Wala Baba Mandir Rajokari	JJC does not exist	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-45	<b>JJC does not exist at site. Hence, no action is required</b>

10780

10781

S.No. of JJ Clusters	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer (Chief Engineer)	Name of EE	Name of EE and Division	Present status
23	Jhuggies Kewal Krishan Chowk Post Rajokari	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-45	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
24	Ram Dev Ka Dera BSF Office Rajokari Pahari, Delhi	Not Feasible	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-45	Not Feasible due to multiple Discharge and collection point. DSTP not feasible due to Forest land. This JJ Cluster may be relocated for reducing pollution. However, discharge is going in low lying area, <b>not in River Yamuna</b>
25	Kusumpur Pahari Block-B Vasant Vihar	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-45	This drain will be trapped by Maintenance Wing after laying approx., 3 Km sewer line by 30.09.2024.
26	Jai Hind Camp near Masoodpur Village Vasant Kunj	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-45	This drain will be trapped by Maintenance Wing after laying approx., 2 Km sewer line by 30.09.2024.
27	Moti Lal Nehru Camp J.N.U	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-45	This drain will be trapped by Maintenance Wing after completion of work of ongoing work of rehabilitation.
28	Junapur Bhim Basti	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-46	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
29	Mandi Pahari (Shambhav Camp)	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Sawant Singh, EE(M)-46 / Sh. A.M. Sharma, EE(C)DR-VI	This JJC can be trapped into DJB sewer line with in one month after completion of sewer network laid by Project wing. The expected date for trapping this drain into sewer line is 30.09.2024 by Maintenance Wing.
30	Mandi Village Bapu Camp	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Sawant Singh, EE(M)-46 / Sh. A.M. Sharma, EE(C)DR-VI	This JJC can be trapped into DJB sewer line with in one month after completion of sewer network laid by Project wing. The expected date for trapping this drain into sewer line is 30.09.2024 by Maintenance Wing.
31	Mandi Village (Biru Camp)	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Sawant Singh, EE(M)-46 / Sh. A.M. Sharma, EE(C)DR-VI	This JJC can be trapped into DJB sewer line with in one month after completion of sewer network laid by Project wing. The expected date for trapping this drain into sewer line is 30.09.2024 by Maintenance Wing.

S.No. of 59 JJC list	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer ( Chief Engineer )	Name of SE	Name of EE and Division	Present status
32	Mandi Village (Shanti Camp)	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Sawant Singh, EE(M)-46 / Sh. A.M. Sharma, EE(C)DR-VI	This JJC can be trapped into DJB sewer line with in one month after completion of sewer network laid by Project wing. The expected date for trapping this drain into sewer line is 30.09.2024 by Maintenance Wing.
33	Dr. Ambedkar Satwari Mehrauli	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-46	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
34	Suhrpuri Mehrauli	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Sawant Singh, EE(M)-46 / Sh. A.M. Sharma, EE(C)DR-VI	Sewer line work is in progress in the vicinity. Therefore drain will be trapped in DJB sewerage network by maintenace wing
35	Kharak Riwara Satwari Mehrauli	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Sawant Singh, EE(M)-46 / Sh. A.M. Sharma, EE(C)DR-VI	Sewer line work is in progress in the vicinity. Therefore drain will be trapped in DJB sewerage network by Maintenance Wing by 30.09.2024
36	Sanjay Colony- Mehrauli Bhatti Mines	Not feasible.	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh. Sawant Singh, EE(M)-46	No JJC found at site. This colony is situated on forest land as informed by area JE (maintenance) having big size plots, wide roads etc. It was also observed during inspection along with NMCG official and JE maintenance that there are so many outfalls of SW drains outfalling in low lying forest area/rocky area.This JJ Cluster may be relocated for reducing pollution.
37	Shanshi Camp Mathura road Badarpur, Tughlakabad	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Satender Dabas,EE(M)-52	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.

10

10782

10783

S.No. of JJCs	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer ( Chief Engineer )	Name of S	Name of EE and Division	Present status
38	Dora Tabu Camp Near Tughlakabad Railway Station in Mohan Co-Operative, Tughlakabad	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Satender Dabas,EE(M)-52	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
39	Indira Camp Alimore Mathura road Mohan Co-Operative, Tughlakabad	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Satender Dabas,EE(M)-52	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of competent authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Further a meeting was held in the chamber of CE(Dr)Proj-III wherein EE(SDW)-V was directed to obtain fresh quotations for DSTP from different vendors and put up the estimate accordingly do that same can be forwarded to NMCG for releasing the fund.
40	Sonia Ganghi Camp Pul-Prahladpur Railway line Tughlakabad	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Satender Dabas, EE(M)-52	This JJC will be trapped into DJB sewer line by 30.09.2024 by Maintenance Wing.
41	Ram Pyari Camp Near Nangia Park Lal kuan, Tughlakabad	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Satender Dabas,EE(M)-52	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.

S.No. of 59 JJC list	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer (Chief Engineer)	Name of SE	Name of EE and Division	Present status
42	Shiv Camp Lal Kuan Badarpur Chungi No proposal.-2 & 3 M.B. Road, Tughlakabad	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Satender Dabas, EE(M)-52	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of competent authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Further a meeting was held in the chamber of CE(Dr)Proj-III wherein EE(SDW)-V was directed to obtain fresh quotations for DSTP from different vendors and put up the estimate accordingly do that same can be forwarded to NMCG for releasing the fund.
43	Khatta Camp Gosain Crusher M.B. Road Lal Kuan, Tughlakabad	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Satender Dabas, EE(M)-52 / Sh. A.M. Sharma, EE(C)DR-VI	Sewer line work is in progress in the vicinity. Therefore drain will be trapped in DJB sewerage network by Maintenance Wing by 30.09.2024
44	Sonia Gandhi Camp Pul-Prahladpur Railway Line Tughlakabad Part-2, Tughlakabad	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Satender Dabas, EE(M)-52	This JJC will be trapped into DJB sewer line by 30.09.2024 by Maintenance Wing.
45	Subash Camp NTPC Badarpur	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11	Sh Manoj Kr. Sharma, EE(M)-53	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
46	BIW JJ Camp B.T. Badarpur	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Manoj Kr. Sharma, EE(M)-53 / Sh. A.M. Sharma, EE(C)DR-VI	Sewer line work is in progress in Gautampuri. Thereafter, drain will be trapped in DJB sewerage network by Maintenance Wing by laying a sewer line by 31.12.2024
47	Tajpur Pahari Badarpur	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)-11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Manoj Kr. Sharma, EE(M)-53 / Sh. A.M. Sharma, EE(C)DR-VI	This JJC will be trapped into DJB sewer line only after laying of sewer network in surrounding UACs which is in approval under EE(C) Dr-VI. Discharge of this JJC is mixing with discharge of UAC also and is collected in a depression/ pond located in between the JJC & UACs. Installation of DSTP is also not feasible as collection of discharge at one point is not feasible. However, the tentative timelines for trapping of this drain into DJB sewer network is 31.12.2024

12

10784

10785

S.No. of JJ Cluster	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer ( Chief Engineer )	Name of SE	Name of EE and Division	Present status
48	Parasad Nagar, Molarband Extn, Badarpur	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)- 11	Sh Manoj Kr. Sharma, EE(M)-53	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
49	Bilas Pur Camp Molar Band NTPC, Badarpur	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)- 11 / Sh. R.K. Lakhera, SE(C) - 4	Sh Manoj Kr. Sharma, EE(M)-53 / Sh. A.M. Sharma, EE(C)DR-VI	This JJC will be trapped into DJB sewer line only after laying of sewer network in surrounding UACs which is in approval under EE(C) Dr-VI. Discharge of this JJC is going into Gurgaon Canal, <b>not in River Yamuna</b> . Installation of DSTP is also not feasible as collection of discharge at one point is not feasible. However, the tentative timelines for trapping of this drain into DJB sewer network is 31.12.2024
50	New Priyanka Camp near Sarita Vihar	Not Feasible	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)- 11	Sh Manoj Kumar Sharma, EE(M)-54	Not feasible because collection of JJC discharge is not possible at single point. However, this discharge of this JJC is falling into Agra Canal, <b>not in River Yamuna</b> . This JJ Cluster may be relocated for reducing pollution.
51	Subhash Camp, Ali Gaon, Near Old Iron Bridge.	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)- 11	Sh Manoj Kr. Sharma, EE )-54	This JJC will be trapped into DJB sewer line by 30.09.2024 by Maintenance Wing.
52	Abul Fazal Enclave Okhla Village Across Canal (Pucca Structure)	30.09.2024	Sh. Gajendra Tomar, CE(South)	Sh B.C Patel, SE (M)- 11	Sh Manoj Kr. Sharma, EE )-54	This JJC will be trapped into DJB sewer line by 30.09.2024 by Maintenance Wing.
53	Pankaj Garden Goela Dairy	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh. Anil Kumar Sharma , SE (M) - 9 / Sh. Adarsh Kumar, SE(DR)Proj-I	Smt. Anjali Nanglot, EE(M)-35 / Sh. R.K Gupta, EE(C)DR-XIV	The work of laying the sewer line in Goela Vihar GoC is in progress. For DSTP at Goela, tenders have been received. The drain will be trapped by Maintenance wing on completion of sewer line and construction of DSTP work.
54	JJC at Goela Dairy Najafgarh	31.12.2024	Sh. Gajendra Tomar, CE(South)	Sh. Anil Kumar Sharma , SE (M) - 9 / Sh. Adarsh Kumar, SE(DR)Proj-I	Smt. Anjali Nanglot, EE(M)-35 / Sh. R.K Gupta, EE(C)DR-XIV	The work of laying the sewer line in Goela Vihar GoC is in progress. For DSTP at Goela, tenders have been received. The drain will be trapped by Maintenance wing on completion of sewer line and construction of DSTP work.
55	Arjun Camp Mahipal Pur	9 months after receipt of funds from NMCG and availability of land for DSTP	Sh. Gajendra Tomar, CE(South)	Sh. Anil Kumar Sharma , SE (M) - 9	Smt. Anjali Nanglot, EE (M) - 36	DPR for feasible sites approved by NMCG after joint inspection is prepared. The DPR and estimate has been checked by planning cell of DJB and sent to NMCG on 28.11.2023 for further action. Referring to the MOM of 8th HLC, the NMCG has intimated DJB on 11.03.2024 stating that they need revised DPR if DJB floats tender on open technology though DJB was of the view that funds may be released considering already submitted estimate & DPR. But, NMCG didn't agree to DJB request & called a meeting in the office of ED, NMCG on 7.5.2024 wherein, it was decided that DJB will prepare new estimate on the basis of fresh quotations & send it to NMCG after approval of the Competent Authority. Thereafter, NMCG will scrutinise it and release the funds on approval of C/A of NMCG. Now, the estimate is being re-framed and will be forwarded to NMCG for releasing the funds shortly.
56	Rangpur Pahari Milkpur Kohi	31.03.2025	Sh. Gajendra Tomar, CE(South)	Sh. Anil Kumar Sharma , SE (M) - 9	Smt. Anjali Nanglot, EE(M)-36	Can be trapped by installing lift station and laying sewer line by maintenance wing.

S.No. of 59 JJC list	Name of JJ Cluster	Revised Timelines for Trapping (Earlier Timeline - June, 2023)	Nodal Officer ( Chief Engineer )	Name of EE	Name of EE and Division	Present status
57	Harijan Balmiki Camp, Rangpur Pahadi	31.03.2025	Sh. Gajendra Tomar, CE(South)	Sh. Anil Kumar Sharma , SE (M) - 9	Smt. Anjali Nanglot, EE(M)-36	Can be trapped by installing lift station and laying sewer line by maintenance wing.
58	Rangpuri Pharai Nalla	31.03.2025	Sh. Gajendra Tomar, CE(South)	Sh. Anil Kumar Sharma , SE (M) - 9	Smt. Anjali Nanglot, EE(M)-36	Can be trapped by installing lift station and laying sewer line by maintenance wing.
59	Nehru Camp Behind Satya Rani Farm Bijwasan	31.03.2025	Sh. Gajendra Tomar, CE(South)	Sh. Anil Kumar Sharma , SE (M) - 9	Smt. Anjali Nanglot, EE(M)-36	Can be trapped by installing lift station and laying sewer line by maintenance wing.

14

10786

### Status of construction of 40 new DSTPs

SNO	Name of DSTP	Capacity in MGD	Present Status	Timelines provided for month April 2024	Timelines provided for month May 2024
1	Mitraon	10.89	Tender stage	31.12.2025	The proposal was placed before the Board for award of work in its last meeting wherein it was decided to take up this work under <b>AMRUT 2.0</b> . Funds are approved under AMRUT 2.0. These tenders are under HAM model which is under review. Further as per the latest guidelines, AA & ES for these estimates are to be approved by UD deptt./ EFC/ GoM as per the cost.
2	Kair	1.1	Tender stage	31.12.2025	Tender under award. Funds are approved under AMRUT 2.0. These tenders are under HAM model which is under review. Further as per the latest guidelines, AA & ES for these estimates are to be approved by UD deptt./ EFC/ GoM as per the cost. Tenders re-invited.
3	Kakrola	2.64			
4	Khanganheri	0.77			
5	Dichaon Kalan	1.98			
6	Punjab Khor	0.22	Tender stage	31.12.2025	Tenders are being reinvited. These tenders were under HAM model which is under review. Further as per the latest guidelines, AA & ES for these estimates are to be approved by UD deptt./ EFC/ GoM as per the cost.
7	Jat Khor	0.22			
8	Qutubgarh	0.66			
9	Auchandi	0.88			
10	Mohammadpur Majri & Karala	2.86	Tender stage	31.12.2025	
11	Kanjhawala & Ladpur	1.1			
12	Nizampur and Sawda	1.32			
13	Garhi Rindhala	0.22			
14	Jaunti	0.44			
15	Ghewra	0.44			
16	Khera Khurd	0.6	Tender stage	31.12.2025	As per the latest guidelines, AA & ES for this estimate is to be approved by UD deptt./ EFC/ GoM as per the cost.
17	Zindpur	15	Tender stage	31.12.2025	Tenders received and under Technical Evaluation. Funds are approved under AMRUT 2.0. These tenders are under HAM model which is under review. Further as per the latest guidelines, AA & ES for this estimate is to be approved by UD deptt./ EFC/ GoM as per the cost.
18	Sarangpur Village	1.32	Tender stage	31.12.2025	During first call single bid was received. The proposal was placed before the Board for award of work and it was directed to re-invite the tenders. Funds are approved under AMRUT 2.0. These tenders are under HAM model which is under review. Further as per the latest guidelines, AA & ES for these estimates are to be approved by UD deptt./ EFC/ GoM as per the cost.
19	Galibpur Village	0.55			
20	Kazipur Village	0.55			
21	Jafarpur Village	1.32			
22	Khera Dabar Village	0.55			
23	Hasanpur Village	1.32			
24	Shikarpur Village	0.66			
25	Chandanhola Satbari	0.44	Tender stage	31.12.2025	Land available, NIT has been finalized, however, as per the new guidelines, AA & ES of the scheme is to be got approved from EFC. Accordingly, the case is being submitted for approval and thereafter the tender will be invited.

26	Tajpur Pahari	10	Tender stage	31.12.2025	Land allotted and taken over. NIT has been finalized, however as per the new guidelines, AA & ES of the scheme to be got approved from EFC. Accordingly, the case is being submitted for approval and thereafter the tender will be invited.
27	Jauna Pur-I	3.18	Tender stage	31.12.2025	Balance land allotted on 02.01.2024 and taken over. NIT has been finalized, however as per the new guidelines, AA & ES of the scheme to be got approved from EFC. Accordingly, the case is being submitted for approval and thereafter the tender will be invited.
28	Jauna Pur-II				
29	Dera Mandi , Bhati				
30	Fatehpur Beri & Asola				
31	Salapur Majra	1.38	Tender stage	31.12.2025	Draft NIT under approval. Further as per the latest guidelines, AA & ES of the these estimates are to be approved by UD deptt./ EFC/ GoM as per the cost.
32	Bajitpur Thakran	2.2			
33	Palla (Sungarpur)	0.44	Estimate stage	Dec-25	Possession of Land taken on 10.08.2023. Estimate for DSTP prepared and under approval. Further as per the latest guidelines, AA & ES for this estimate is to be approved by UD deptt./ EFC/ GoM as per the cost.
34	Tajpur	1.1			
35	Rangpuri	5	Estimate stage	31.12.2025	For construction of STP & SPS, DDA have been allotted lands to DJB. Payment has been processed
36	Chattarpur Extension	0.38	Estimate stage	31.12.2025	1525.25 sqm land has been allotted on 05.03.2024 out of 4 Bigha 4 Biswa. Payment amounting to Rs. 384.24 lac was deposited to DDA vide EE(C)Dr.-VI letter dated 17.05.2024. Possession of land is yet to be handed over by DDA.
37	Maidan Garhi (Rajpur Khurd)	0.95	Land issue	18 Months after handing over the possession of land to DJB	Land yet to be allotted
38	Nayabans	4.4			
39	Tajpur Khurd	7.92	Estimate stage	31.12.2025	Land handed over on 21.06.2024. Scheme taken up accordingly. Estimates is being prepared.
40	Tikri Kalan	1.32	Estimate stage	31.12.2025	Land handed over on 01.07.2024. Scheme taken up accordingly. Estimates is being prepared.


# Water Quality of Untapped Outfalling Drains into Yamuna (Jan., 2023 & Jan., 2024)

ANNEXURE-IV


S.No.	Name of Drain	TSS (mg/l)		COD (mg/l)		BOD (mg/l)	
		Jan, 2023	Jan, 2024	Jan, 2023	Jan, 2024	Jan, 2023	Jan, 2024
Standards		100		250		30	
1	Najafgarh	120	88	272	232	53	43
2	ISBT Drain (Qudsia Bagh/ Mori Gate)	124	80	208	192	44	39
3	Sen Nursing Home	132	86	266	224	50	40
4	Delhi Gate/(Power House)	112	78	224	186	53	38
5	Sonia Vihar	136	82	320	160	63	33
6	Kailash Nagar	124	70	176	170	58	36
7	Shastri Park	68	56	208	152	40	24
8	Barapulla	88	76	213	213	43	38
9	Maharani Bagh	92	84	186	220	46	41
10	Jaitpur	108	72	176	196	48	37
11	Tuglakabad	168	66	264	172	64	36
12	Shahdara	112	94	272	266	60	47

# Yamuna Water Quality : BOD (mg/l) variation [ Stds ≤ 3mg/l ] 10790


Najafgarh Drain

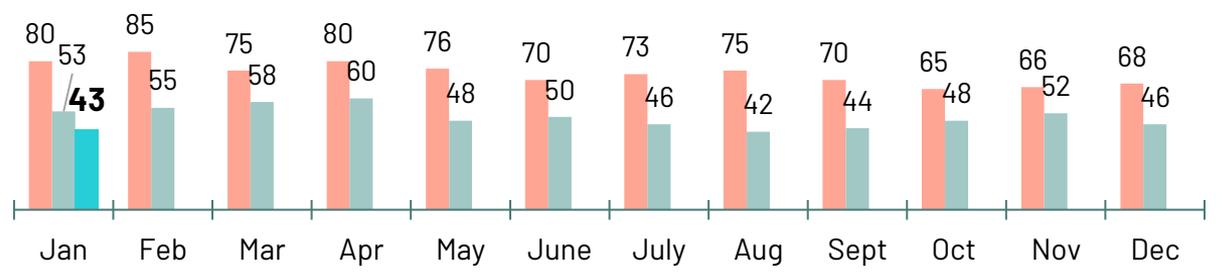

ISBT (After meeting Najafgarh Drain)



Asgarpur (D/s of Okhla Barrage after confluence of Shahdara & Tuglakabad drains)



**Year: 2022**


**Year: 2023**

**Year: 2024**




# Yamuna Water Quality : FC (mg/l) variation [Stds ≤ 2500 MPN/100ml]

ISBT (After meeting Najafgarh Drain)

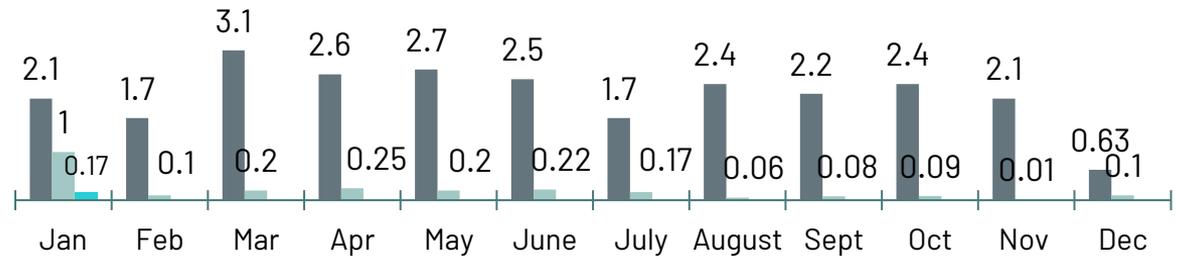

Values in Lakhs

Asgarpur (D/s of Okhla Barrage after confluence of Shahdara & Tuglakabad drains)

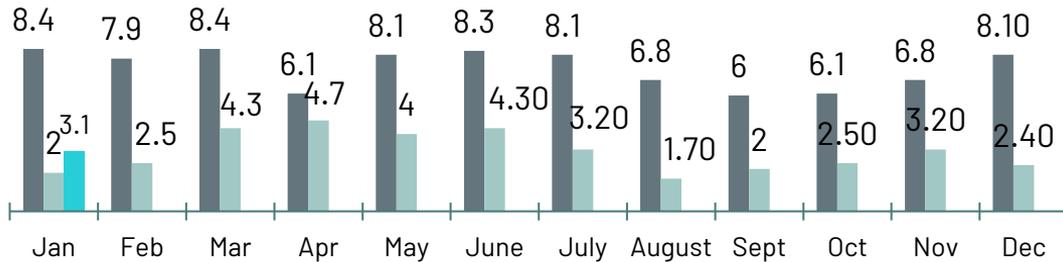

Values in Lakhs

- Year: 2022
- Year: 2023
- Year: 2024

### Details of 10 Nos. Trapped Drain receiving treatment at STPs

S. No.	Name of Drain	Flow in MLD (MGD)			Status of Drain (Trapped / Partially Trapped / Untrapped)	STP in which trapped waste water is treated		Proposed Action/ Timeline for Tapping of Drain
		Total Waste Water	Treated Waste water	Untreated Waste water		Name	End Point of Disposal	
1.	Metcalf House Drain	17.25 (3.79 MGD)	-	17.25 (trapped & get treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/IV/V/VI)	Agra canal. Discharge treated effluent in Agra Canal is being used for irrigation purpose.	New 124 MGD STP at Okhla has started treating 48 MGD of sewerage from 01.04.2024. The plant is under trial run and commissioning which will be completed on <b>30.09.2024</b> .
2.	Khyber Pass Drain	1.7 (0.37 MGD)	-	1.7 (trapped & treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/IV/V/VI)		

3.	Sweeper Colony Drain	8.6 (1.89 MGD)	-	8.6 (trapped & treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/IV/V/VI)		
4.	Magazine Road Drain	7.8 (1.72 MGD)	-	7.8 (trapped & treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/IV/V/VI)	Agra canal. Discharge treated effluent in Agra Canal is being used for irrigation purpose.	New 124 MGD STP at Okhla has started treating 48 MGD of sewerage from 01.04.2024. The plant is under trial run and commissioning which will be completed on <b>30.09.2024</b> .
5.	Tonga Stand Drain	7.8 (1.72 MGD)	-	7.8(trapped & treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/IV/V/VI)		
6.	Civil Mill Drain	14.68 (3.23 MGD)	-	14.68 (trapped & treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/IV/V/VI)		

7.	Moat Drain (Vijay Ghat)	Dry	-	(trapped & treated at Okhla STP)	Trapped (but no flow at present)	Okhla STP (Phase II/III/ IV/V/VI)		
8.	Drain No. 14	25.87 (5.69 MGD)	-	25.87 (trapped & treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/ IV/V/VI)		
9.	Tehkhand Drain	39.74 (8.74 MGD)	-	39.74 (trapped & treated at Okhla STP)	Trapped	Okhla STP (Phase II/III/ IV/V/VI)	Agra canal. Discharge treated effluent in Agra Canal is being used for irrigation purpose.	New 124 MGD STP at Okhla has started treating 48 MGD of sewerage from 01.04.2024. The plant is under trial run and commissioning which will be completed on <b>30.09.2024</b> .
10.	Tuglakabad Drain (Kalka Ji Drain merged in this drain)	25.05 (5.51 MGD)	-	25.05	Trapped	Okhla STP (Phase II/III/ IV/V/VI)		
	<b>Total</b>	<b>148.49</b>		<b>148.49</b>				

### Details of Partially trapped drains

S. No.	Name of Drain	Flow in MLD (MGD)			Status of Drain (Trapped / Partially Trapped / Un trapped)	STP in which trapped waste water is treated		Proposed Action/ Timeline for Tapping of Drain
		Total Waste Water	Treated Waste water	Untreated Waste water		Name	End Point of Disposal	
1.	Sen Nursing Home Drain	43.2 (9.5 MGD)	10	33.2	Partially trapped	Sen Nursing Home STP (10 MLD)	Yamuna River	Entire flow of the drain shall be trapped and taken to Okhla STP after construction/commissioning of Maharani Bagh SPS and desilting of Ring Road trunk sewer by <b>June-2025</b> .
2.	Delhi Gate Drain / Power House Drain	122.58 (26.96 MGD)	78	44.58	Partially trapped	Delhi Gate STP	Yamuna River	<ul style="list-style-type: none"> <li>There are 2 operational STPs of 68.2 MLD (15 MGD) capacity and 10 MLD (2.2 MGD) capacity for treatment of trapped wastewater of this drain.</li> <li>Another STP of 45.46 MLD (10 MGD) is proposed for the treatment of remaining untrapped waste water of this drain. Land allotted by MoHUA/DDA. Payment is being made.</li> </ul>
	<b>Total</b>	<b>165.78</b>	<b>88</b>	<b>77.78</b>				

### Details of 2 large drain (Najafgarh & Shahdra ) not feasible to trapped

S. No.	Name of Drain	Flow in MLD (MGD)			Status of Drain(Trapped / Partially Trapped / Untrapped)	STP in which trapped waste water is treated		Proposed Action/ Timeline for Tapping of Drain																
		Total Waste Water	Treated Waste water	Untreated Waste water		Name	End Point of Disposal																	
1.	Najafgarh Drain	2056.32 (452.34 MGD)	1380	676.32	Being large drain not feasible to be trapped	-	Yamuna River	<p>ISP has been commissioned and provision for tapping of 77 drains have been made.</p> <p>There is about 453 MGD flow in the Najafgarh drain. Out of this at present 303.85 MGD comprises of treated effluent from STPs. From Haryana, untreated discharge of 105 MGD is being discharged through Badshahpur and DD-6 drains.</p> <p>Details of STP at different location whose treated effluent 1380 MLD (303.85 MGD) is falling into Najafgarh drain:</p> <table border="1"> <thead> <tr> <th>Location</th> <th>Falling into Najafgarh drain in MGD</th> </tr> </thead> <tbody> <tr> <td>Keshopur Ph-I, II &amp; III</td> <td>66.5</td> </tr> <tr> <td>Nilothi Ph-I, II</td> <td>58.5</td> </tr> <tr> <td>Papankalan Ph-I, II</td> <td>36.67</td> </tr> <tr> <td>Najafgarh</td> <td>4.43</td> </tr> <tr> <td>Kapashera</td> <td>4.5</td> </tr> <tr> <td>Coronation Pillar</td> <td>56.5</td> </tr> <tr> <td>Rithala</td> <td>67</td> </tr> </tbody> </table>	Location	Falling into Najafgarh drain in MGD	Keshopur Ph-I, II & III	66.5	Nilothi Ph-I, II	58.5	Papankalan Ph-I, II	36.67	Najafgarh	4.43	Kapashera	4.5	Coronation Pillar	56.5	Rithala	67
Location	Falling into Najafgarh drain in MGD																							
Keshopur Ph-I, II & III	66.5																							
Nilothi Ph-I, II	58.5																							
Papankalan Ph-I, II	36.67																							
Najafgarh	4.43																							
Kapashera	4.5																							
Coronation Pillar	56.5																							
Rithala	67																							

								Rohini	9.75	
								<b>Total</b>	<b>303.85</b>	
2.	Shahdara Drain	840 (184.78 MGD)	363	477	Being large drain not feasible to be trapped	-	Yamuna River	<p>ISP has been commissioned and provisions for tapping of 29 drains have been made.</p> <p>Total untreated discharge in Shahdara drain is about 105 MGD, out of which 50 MGD (i.e., 45%) is untreated sewage is being discharged by UP through Sahibabad, Indirapuri and Banthala drain.</p> <p>treated effluent from Kondli STP &amp; Chilla STP of about 363 MLD (80 MGD) is falling into Shahdara Drain</p>		
	<b>Total</b>	<b>2896.32</b>	<b>1743</b>	<b>1153.32</b>						

### Details of 08 nos. to be trapped drains

S. No	Name of Drain	Flow in MLD (MGD)			Status of Drain (Trapped / Partially Trapped / Untrapped)	STP in which trapped waste water is treated		Proposed Action/ Timeline for Tapping of Drain
		Total Waste Water	Treated Waste water	Untreated Waste water		Name	End Point of Disposal	
1.	Abul Fazal Drain	7 (1.54 MGD)	-	7	To be trapped	-	-	Sewage to be trapped after completion of Batla House Sewage scheme and expected to be completed by <b>Dec-2024</b> . Trapped waste water will be treated at Okhla STP.
2.	ISBT Drain (Qudsia Bagh/ Mori Gate Drain)	20.80 (4.58 MGD)	-	20.80	To be trapped	-	Yamuna River	Work of construction of SPS at the outfall point of the drain is in progress and likely to be completed by <b>Dec-2024</b> . Trapped waste water will be treated at Coronation Piller STP
3.	Sonia Vihar Drain (On Eastern Bank of Yamuna)	27.24 (5.99 MGD)	-	27.24	To be trapped	-	Yamuna River	7 MGD STP is being constructed at Sonia Vihar which is likely to be completed by <b>October- 2024</b> . Trapped waste water will be treated at Sonia Vihar STP
4.	Kailash Nagar Drain (On Eastern Bank of Yamuna)	13.62 (3.0 MGD)	-	13.62	To be trapped	-	Yamuna River	Feasibility of diverting the flow of the drain to Kondli STP through Geeta Colony and Preet Vihar SPS is being worked out jointly with MCD, DUSIB, DDA and DJB.

5.	Shastri Park Drain(On Eastern Bank of Yamuna)	5.45 (1.2 MGD)	-	5.45	To be trapped	-	Yamuna River	Feasibility of construction of DSTP is being worked out jointly with MCD, DUSIB, DDA and DJB..
6.	Maharani Bagh Drain	30.24 (6.65 MGD)	-	30.24	To be trapped	-	Yamuna River	Work of Intercepting the Maharani Bagh drain flow by laying of interceptor sewer through micro tunneling and conveying the flow to Okhla WWTP for treatment is in progress and expected to be completed by <b>Dec-2024</b> .
7.	Jaitpur Drain	5.68 (1.25 MGD)	-	5.68	To be trapped	-	Yamuna river	Sewage to be trapped after completion of Madanpur Khadar GOC scheme by <b>Dec-2025</b> . Trapped waste water will be treated at Okhla STP.
8.	Barapulla Drain	91 (20 MGD)	-	91	To be trapped	-	Yamuna River	Work of Intercepting the Barapullah drain flow by laying of interceptor sewer through micro tunneling and conveying the flow to Okhla WWTP for treatment is in progress and expected to be completed by <b>Dec-2024</b>
	<b>Total</b>	<b>201.03</b>		<b>201.03</b>				
