

**DEPARTMENT OF URBAN DEVELOPMENT  
GOVERNMENT OF UTTAR PRADESH**

Date: 01.02.2021

To,

**The Registrar**

National Green Tribunal

Principal Bench

New Delhi.

**Subject:** Action Taken Report in O.A. No: 209/ 2019

Hon'ble National Green Tribunal in above O.A. No: 209/2019 have ordered on 30.07.2020 on the matter mainly pertaining to unscientific management and dumping of Solid waste in Loni Nagar Palika Parishad.

The updated status on the compliance points are as following:

S.N.	Points	Updated Status/ Action Taken
1	Setting up of Scientific Landfill Site and Processing Facility at Meerpur Hindu and the bio- remediation of the Legacy Waste.	The work for the construction of processing facility amounting 17.28 Cr. is under progress and completed by 35%. The work of construction if being done by the executive agency C&DS ( Construction & Design Services) - UP Jal Nigam nominated by the Urban Development Department Uttar Pradesh. A progress report sought from the C&DS UP Jal Nigam is attached here with for your reference as <b>Annexure-1</b> . Due to Mansoon season the work of Bio-remediation of the legacy waste was started in the month of October and under progress, which is to be completed in next 4 months time as reported from the NPP Loni. The reference photographs of the ongoing work are attached here in PPT prepared by NPP Loni is attached as <b>Annexure-2</b> .
2	Regular monitoring of the compliances in Nagar Palika Parishad Loni.	It's being regularly monitored with the district administration and the executive agency C&DS for the progress of the work. As submitted earlier the processing facility is likely to be completed and made functional within 6 months time.
3	The current status of solid waste management in Nagar Palika Parishad Loni, District Ghaziabad.	The ULB has end the contract with the previous agency and hired the new one for the door to door collection and transportation with the new set of vehicle and other

	facilities and started working from the date of 1 <sup>st</sup> December 2020. The waste collection in the town is being done by the 46 no of tricycles +55 No of tipper + 75 No of tractors and 7 bigger vehicles ( Hopper dumper) for the secondary waste collection, out of total 137 Motorised vehicle all vehicles have the GPS devices for primary & secondary waste collection are GPS Enabled, the online report of the respective GPS enabled vehicle is generated on daily basis for the record. It is submitted by the Nagar Palika Parishad that the waste is being collected and transported in the covered vehicles. The reference pictures are mentioned in the <b>Annexure-2</b> .
--	--

It is submitted before this Hon'ble Tribunal that the Department has always been committed to ensure compliance of SWM Rules and directions of this Hon'ble Tribunal. There has been a lot of resistance from local poulace against setting up a scientific waste processing plant, especially due to not in my backyard syndrome, this had delayed the work. However with a lot of sincere efforts and co-operation of local official, the peaceful possession of land could be achieved for construction work and securing the site with boundary wall and it is already done. The other work related to setting up of plant is underway and as of now the work progress achieved is 35% the entire work is scheduled to be completed in next 6 months' time. It is humbly submitted that the progress of work has also suffered due to COVID-19 Pandemic situation and lockdown as this area was highly affected. However, the compliance as per Hon'ble Tribunal's order shall be ensured by proper monitoring. The updated status of compliance and progress being made has also been submitted to Oversight Committee chaired by Hon'ble Justice (Rtd.) Shri S.V.S. Rathore.

  
**Deepak Kumar**  
Principal Secretary  
Department of Urban Development

सॉलिड वेस्ट मैनेजमेंट योजना लोनी की अद्यतन स्थिति का विवरण।

प्रशनगत परियोजना की पुनरीक्षित लागत शासनादेश संख्या 4740/नौ-5-2020-418 सा/2018 दिनांक 21.10.2020 नगर विकास अनुभाग-5, उत्तर प्रदेश शासन के माध्यम से रू0 1728.00 लाख की स्वीकृत की गयी है। जिसके अन्तर्गत 275 टन प्रति दिन ठोस अपशिष्ट के प्रबन्धन हेतु सॉलिड वेस्ट मैनेजमेंट प्लान्ट सिविल पार्ट (वेस्ट टू कम्पोस्ट आधारित) का निर्माण कार्य कार्यदायी संस्था सी0एण्ड डी0एस0 द्वारा कराया जा रहा है।

कार्यस्थल पर चाहरदीवारी का निर्माण कार्य पूर्ण कर लिया गया है तथा प्लान्ट का निर्माण कार्य निविदा इत्यादि पूर्ण करते हुए दिनांक 20.11.2020 को प्रारम्भ कर दिया गया है, एवं कार्य पूर्ण करने की लक्षित तिथि 19.05.2021 निर्धारित है। वर्तमान में परियोजना में स्वीकृत मानसून शेड, वर्कशॉप शेड, लीचेट ड्रेन, वेस्ट रिसीविंग एरिया, विन्ड्रो प्लैटफॉर्म, लीचेट टैंक, गार्ड रूम, वे ब्रिज रूम, एच0टी0एल0टी0 पैनल रूम, जनरेटर रूम का कार्य प्रगति पर है तथा वर्तमान में परियोजना की भौतिक प्रगति 35 प्रतिशत है।



परियोजना प्रबन्धक

**OFFICE OF THE PROJECT MANAGER C & D S.U.P. JAL NIGAM UNIT-31 GHAZIABAD**  
**Name of Scheme - Solid Waste Management, Loni (Ghaziabad)**

Progress : 01/2021

(Amount Rs. Lac)

S.No.	Particulars	S.No.	Particulars	(Amount Rs. Lac)
1	Estimated Cost (Rs. in Lacs)	17	Status of Fund Released to C&DS	590.63
	a) Central Share (Rs. In Lacs)		a) Central Share (Rs. In Lacs)	-
	b) States Share (Rs. In Lacs)		b) States Share (Rs. In Lacs)	-
	c) Local body Share (Rs. In Lacs)		c) Local body Share (Rs. In Lacs)	-
2	Date of Sanction		Total (a+b+c)	590.63
3	Grant ( As Per DPR) (Rs. In Lacs)	18	Solid Waste Generated At Present(2020) in T.P.D.	275 TPD
4	Opreater's Share (As Per DPR)	19	Projected Qty of Solid Waste (As Per DPR)	584.10 MT
5	Land Required/Available (Hactare)		a) Base Year/Qty ( In TPD)	2020 / 275
6	Date of Possession of Land		b) Ultimate Year ( In TPD)	2035 / 584.10
7	No of Wards	20	Installed Capacity of Pre-Sorting Unit (For Year 2020)	20 TPH
8	No of Wards Where Door To Door Collection is Being Done		a) No./Capacity of Each Unit (In TPD)	275
9	Cost of Agreement	21	Expenditure Up To Date:	
10	Date of Start of Work(As Per Agreement)		a) Against Grant (Rs. In Lacs)	375.570
11	Date of Completion of Work (As Per CB)			
12	Rate of Tipping Fee(Rs. Per Tonne)( As Per CB )			
13	O&M Fee (Per Tonne)( As Per CB)			
14	Grant (As per CB)			
15	Opreater's Share (As Per CB)			
16	Status of EIA* Clearance With Date			

\* Environmental Impact Assessment

Resident Engineer

Project Manager

OFFICE OF THE PROJECT MANAGER, C & D S, U.P. JAL NIGAM, UNIT-31, GHAZIABAD

Name of Scheme - Solid Waste Management, Loni (Ghaziabad)

Physical & Financial Progress

Against Grant				
S.No.	Work	Qty Proposed	Target as per Pert Chart	Progress
1	Site Clearance And levelling	8.265 Hact.	28/11/2020	100%
2	Guard Room	27.89 Sqm	05/02/2021	25%
3	Finished Goods Godown	916.67 Sqm	15/04/2021	5%
4	Weigh Bridge	2 Nos	30/04/2021	0%
5	Tipping Floor/ waste Receiving Area	3300 Sqm	28/02/2021	10%
6	Pre-processing Area	1210 Sqm	31/03/2021	25%
7	Compost Pad	16500 Sqm	28/02/2021	-
8	Compost Processing Shed	390 Sqm	20/03/2021	-
9	Monsoon Shed	4550 Sqm	31/03/2021	35%
10	Leachate Collection & Treatment Unit	70 KL 2 Nos	31/03/2021	0%
11	Water Supply System	Job	30/04/2021	0%
12	Power Connection	1 Set	30/04/2021	0%
13	Boundary Wall	1707.00 RM	11/09/2020	100%
16	Overall Progress	-	31/05/2021	35%

Resident Engineer

Project Manager

## कार्यालय परियोजना प्रबन्धक यूनिट-31 सी0 एण्ड डी0 एस0 उ0 प्र0 जल निगम गाजियाबाद

योजना का नाम - सॉलिड वेस्ट मैनेजमेन्ट, लोनी जनपद गाजियाबाद।

स्वच्छ भारत मिशन

(नोडल विभाग नगर विकास)

मण्डल - मेरठ  
प्रगति माह - 01 / 2021

वर्ष - 2020

क्र०	परियोजना का नाम	भौतिक प्रगति										डोर-टू-डोर		टी0 एण्ड पी0 की स्थिति		रू० लाख में				रू० लाख में	
		ड्रिपिंग हेतु भूमि की आवश्यकता	उपलब्ध (एकड़ में)	ड्रान्सपर हेतु भूमि की आवश्यकता	उपलब्ध	साइट पर मशीन के क्रियाशील होने की स्थिति	वातू होने की प्रस्तावित तिथि	साइट तक जाने हेतु सम्पर्क मार्ग निर्माण की स्थिति	है	नहीं	वाडों की कुल संख्या	वाडों की संख्या जहां लागू है	डीपीआर के अनुसार स्वीकृत संयंत्रों की संख्या	उपलब्ध/क्रय किये गये संयंत्रों की संख्या	यूजर चार्ज की स्थिति	(लागू है / लागू नहीं)	यूजर चार्ज के अन्तर्गत वसूली गयी धनराशि	आपरेटर को भुगतान की गयी धनराशि	कलैक्शन एवं ट्रान्सपोर्टेशन से सम्भावित बचत	वास्तविक बचत	
1	लोनी नगर पालिका परिषद	10.00	20.00	-	-	-	-	-	-	55	-	936	674	-	-	-	-	-	-	20	

नोट :- कार्य प्रगति पर।

स्थानिक अभियन्ता

परियोजना प्रबन्धक



# NAGAR PALIKA PARISHAD, LONI, GHAZIABAD

## SOLID WASTE MANAGEMENT

# INTRODUCTION

Loni governed by Nagar Palika Parishad in Ghaziabad district in NCR having coordinates 28.75 degree North and 77.28 degree East. It is most populous corporation in western up having population of 506082 as per census 2011 with a floating population of 10-12 lacs being daily factories workers in the vicinities of Delhi and NCR . Loni NPP has total 55 wards consisting of 95463 houses ,21500 shops and 364 factories. In this area there are total 5 hospitals (one govt hospital and 4 privates ) , total 6 banks ,276 schools ,76 marriages-halls and 4 cinema halls .

In this regard I want to update that we go through average population density of the world its 51 person per square km whereas in new Delhi its 11320 person per Square km. Delhi being capital city has more than one third area as lute in Delhi having much of open area like greens and park and so many things but if we calculate population density excluding lute in area its like loni city ..har taraf har taraf beshumar aadami...like position. Any way loni non of the less than chandani chowk .Its the nearest place to connect industrial area of Delhi like sarita vihar and okhla etc so having so much of floating population as daily and weekly commuters and making situations more grave so far municipal arrangements are concerned.





# WORK STARTED BY NAGAR PALIKA PARISHAD, LONI, GHAZIABAD WITH M/S-GURU JI INFRASTRUCTURE PVT. LTD.



# PROTECTIVE EQUIPMENTS DISTRIBUTION TO ALL EMPLOYEES



# IEC ACTIVITIES AND CAPACITY BUILDING




# DOOR TO DOOR COLLECTION IN NPP, LONI



# SEGREGATION OF WASTE IN NPP, LONI



# SWEEPING WORK IN RESIDENTIAL AREA

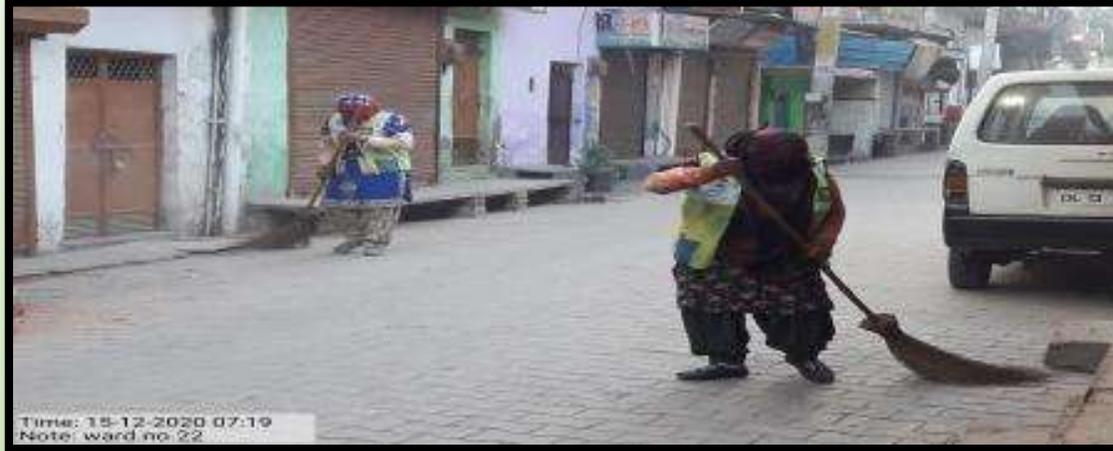

# SWEEPING WORK IN COMMERCIAL AREA




# NIGHT SWEEPING IN LONI



# NALA SAFAI WORK IN LONI



# WORK FOR CONTROL AIR POLLUTION

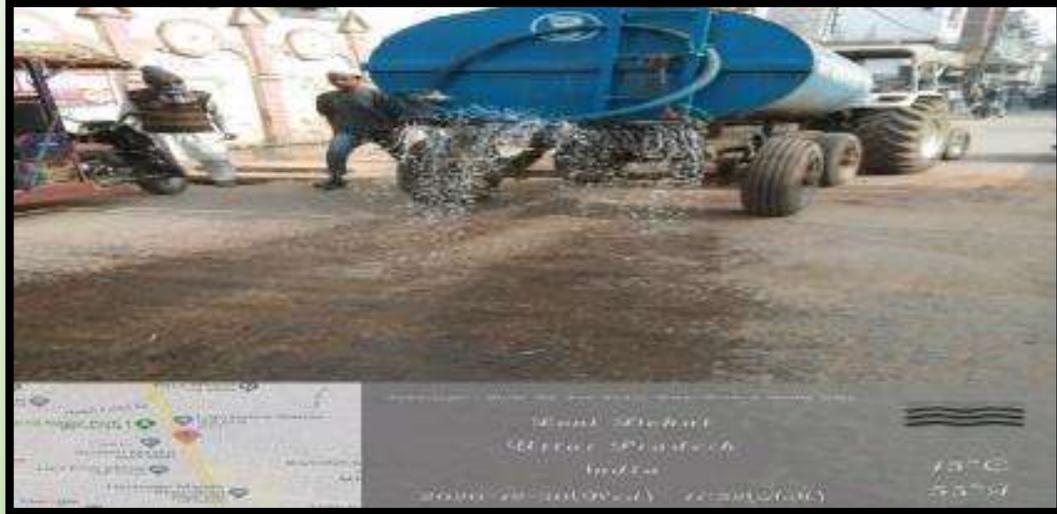

# VEHICLE COVERED BY GREEN TIRPAL





# PIT COMPOSTING



# BIO-REMEDIATION WORK AT UNDER PROCESS



# SOLID WASTE MANAGEMENT PLANT UNDER CONSTRUCTION WORK DONE BY C. & D.S., U.P. JAL NIGAM



# M.R.F. CENTRE UNDER CONSTRUCTION WORK DONE BY N.P.P. LONI



# FOGGING AND ANTILARVA WORK IN LONI



## SANITIAZATION WORK IN LONI



# HEALTH CHECKUP IN LONI



# IEC & AWARENESS CAMPAIGN



# THEME PAINTING IN LONI



# POLYTHENE BAN



# PLANTATION IN LONI



# SOCIAL MEDIA ACTIVITIES









## लोनी नगर पालिका परिषद में स्थापित की गई कोविड-19 केयर हेल्प डेस्क

साखार खड्ड

लोनी। आमजन कोरोना वायरस के संक्रमण को रोकथाम के लिए निम्न अधिकारी अथवा स्टाफ पॉस्ट के निर्देश पर लोनी नगर पालिका परिषद कार्यलय पर कोविड केयर हेल्प डेस्क की स्थापना की गई। यहाँ जॉन्स के बाद कार्यलय में जाने वाले कर्मचारी और लोगों को चेता लगाया जा सके कि कोविड कोरोना वायरस से संक्रमित व्यक्ति अंदर न आ सके। नगर परिषद और सहस्रल लोनी का एक ही जगह होने की वजह से भीड़ हो जाती है। इसलिए कार्यलय में पहुँचने वाले कर्मचारी और आम लोगों को गर्मल स्प्रैयिंग और हाथों को सेनेटाइज करवा जा रहा। साथ ही इस दौरान हेल्प डेस्क पर तैयार कर्मचारी द्वारा कोरोना संक्रमण



लोनी नगर पालिका में कोविड-19 हेल्प डेस्क।

से एहतियात बरतने के बारे में भी लोगों को जागरूक किया जा रहा है। लोनी नगर पालिका

परिषद की अधिकाारी अधिकारी शशिनी गुज्ज ने बताया कि निम्नलिखित के निर्देश पर नगरपालिका परिषद में कोविड केयर हेल्प डेस्क स्थापित की गई। हेल्प डेस्क पर फस अडिमीनीटर इंपरिनेड बयोमीटर स्क्रीनिंग के साथ-साथ सैनिटाइजर फास्क और फ्लाय की व्यवस्था की गई है। इस दौरान नगर पालिका परिषद के सभी कर्मचारी को भी एहतियात बरतने के लिए निर्देश दिया गया है। हेल्प डेस्क पर सेक्टर लक्ष्मण अल्लुओ और कर्मचारी को कोरोना संक्रमण से बचने के लिए साफका हाथ धोने साइडलाइंड के बारे में बताया जा रहा है। इस दौरान लोगों को अस्वस्थ सेतु एप डाउनलोड करने और कोविड संक्रमण से संश्लित जानकारी के लिए स्वास्थ विभाग का नंबर भी सूचित करवा जा रहा है।

## नगरपालिका करेगी सरकारी स्कूलों का काया कल्प

लोनी (कॉन्ट्रि ब्राउज़)। लोनी क्षेत्र में बने बेसिक शिक्षा के स्कूलों में अब नगर पालिका की ओर से छात्रों की सुविधाओं के लिए काम किया जाएगा। जिस स्कूल में जो कमी होगी उसकी पूर्ति नगर पालिका की ओर से की जाएगी। स्कूलों में परामर्श देने के बाद नगर पालिका ने इसकी लेकर अपनी विभागों को शुरु कर दिया। इसी नगर में मौजूद स्कूलों में इनका काम है इसकी लेबर भीयरट से सर्वे रिपोर्ट बने स्कूलों पर सर्वे किया है। सामान्य 10 स्कूलों के बारे में बाद ईओ शशिनी गुज्ज ने बताया कि किसी न किसी रूप में सभी स्कूलों में काम किया जाएगा।



के अलावा पर अब लोनी स्कूलों में काम करने की जिम्मेदारी नगर पालिका की ही गई है। सामान्य के इस प्रकार के बाद नगर पालिका ने इसकी लेबर काउन्सिल को शुरु किया है। लोनी में बेसिक शिक्षा के 22 प्राथमिक और 6 जूनियर हाईस्कूल एवं 10 कॉम्पोजिट स्कूल अंतर्गत हैं। यहाँ पर छात्रों के लिए सौभाग्य, पानी, साफ सुकट और बैटने को व्यवस्था सहित कई बिंदुओं पर काम होने पर नगर पालिका को ही अपने आंक लेबा साखार की ओर से मिले निर्देश में लोनी स्कूलों में नगर पालिका की ओर से हाथ और हाकड़ों के लिए आसम अलग सेक्शनल हैडक्वार्टिस सिस्टम, पानी निकासी, स्कूल की मरम्मत करने, गेट, कार्टड्रिगल का

निर्माण और पानीपर की व्यवस्था करवा है। यहाँ है कि इसी साल का बेसिक शिक्षा का पत्रने काम खर्च भी कम हो जाएगा और छात्रों को बेहतर सुविधा मिल सकेगी। स्कूलों में काम करने के लिए नगर पालिका ने एडिटर प्रमोद कुमार से लोनी में मौजूद स्कूलों की सुची की मांग है। इसकी अलावा ईओ शशिनी गुज्ज ने सभी स्कूलों पर मौजूद छात्रों की को जानकारी भी है लोनी किसी न किसी रूप से काम हो सके इसी शशिनी गुज्ज ने बताया कि भीयरट से स्कूलों की सुची को मांगे गई है और सर्वे के अलावा पर वहाँ छात्रों को देखा जाएगा। 14 से मिले का फिर और किसी तरह से वहाँ पर काम कराया जाएगा। स्कूलों से और बेसिक शिक्षा विभाग से पैसा पत्र आया था।

### लोनी नगर पालिका अधिकाारी अधिकारी ने वन महोत्सव पर की पौधरोपण की शुरुआत : शालिनी गुप्ता

विजय क्षेत्र में लगवाए गए सैकड़ों पौधे

साखार खड्ड

लोनी। वनविभाग की विभाग मुख्यालय में लोनी अधिकाारी अधिकारी शशिनी गुज्ज ने वन महोत्सव पर की पौधरोपण की शुरुआत की। इस अवसर पर शशिनी गुज्ज ने वन विभाग के अधिकारी अधिकारी शशिनी गुज्ज को पौधरोपण करवाती हुई।

शशिनी गुज्ज ने वन विभाग के अधिकारी अधिकारी शशिनी गुज्ज को पौधरोपण करवाती हुई।

शशिनी गुज्ज ने वन विभाग के अधिकारी अधिकारी शशिनी गुज्ज को पौधरोपण करवाती हुई।

