

BEFORE THE NATIONAL GREEN TRIBUNAL, PRINCIPAL BENCH, NEW DELHI  
O.A. NO. 537/2022

MUKESH KUMAR CHAUHAN

--- APPLICANT

VERSUS

STATE OF UTTAR PRADESH & ORS.

---- RESPONDENTS

N.D.O.H. :-19.03.2025


**ACTION TAKEN REPORT/STATUS REPORT ON SANCTIONED WORK FOR UPGRADATION OF HARDUAGANJ GOODS SHED TO CONTROL/ABATEMENT OF ENVIRONMENTAL POLLUTION ON BEHALF OF DRM, NORTH CENTRAL RAILWAY, PRAYAGRAJ, UTTAR PRADESH**

Details of works sanctioned are attached herewith as **annexure-1** and images showing their status are attached herewith as **annexure-2**.

A total amount of Rs. 27,60,95,000 has been sanctioned for upgradation of Harduaganj goods shed.

Pointwise works sanctioned and their status are as follows-

S. N.	WORK SANCTIONED	STATUS OF WORK
1.	Boundary wall-700m	<ul style="list-style-type: none"> <li>• Work of boundary wall along with sheet covering has been completed.</li> <li>• In addition to this, plantation along the boundary wall fence is also being done.</li> </ul>
2.	Track work for full operation (750m from 360m)	<ul style="list-style-type: none"> <li>• Track work has been completed</li> </ul>
3.	Earth filling-14700 cubic m (currently increased up to 49100 cubic m)	<ul style="list-style-type: none"> <li>• Earth filling work has been completed.</li> </ul>
4.	Provision of heavy duty wharf (700m x 30m x 0.6m)	<ul style="list-style-type: none"> <li>• Work of wharf wall for line no. 15 has been completed. Work of wharf of line no. 15 has been completed approx. 175 x 14 m.</li> </ul>
5..	Proper drainage system(2x700m)	<ul style="list-style-type: none"> <li>• RCC drain work has been completed.</li> </ul>
6.	Approach road RCC-1800m	<ul style="list-style-type: none"> <li>• Work is under progress</li> </ul>
7.	High Mast Tower-02	<ul style="list-style-type: none"> <li>• Work is under progress</li> </ul>

  
(Himansu Badoni)  
D.R.M./N.C Railway  
Prayagraj

8.	Provision of CCTVs for monitoring loading & unloading areas.	<ul style="list-style-type: none"> <li>• After the completion of entire work, CCTVs will be installed within a week time.</li> </ul>
----	--	--

Tentative date for completion of sanctioned work is **April-2025**.

In addition to above, to control pollution of air and water, other necessary actions have been taken at Harduaganj goods shed which are as under-

1. As the approach road to Harduaganj goods shed is unpaved, to prevent dust from flying due to the movement of trucks and to avoid any adverse effect on human life as well as the health of wild animals and birds, during unloading of clinker, water is continuously sprayed from tankers on the entire road and loading/unloading area.
2. During loading/unloading of clinker in line no. 14 of Harduaganj Goods Shed, 02 pieces of portable anti-smoke guns are used so that the clinker dust does not cause air pollution in the environment.
3. To control the fugitive dust generated due to loading/unloading of clinker in Harduaganj Railway Goods Shed, it has been covered with a boundary of about 700 meters long and 20 feet high with long sheet on both sides from east and west side of the railway station. So far around 600 plants have been planted at Harduaganj station and goods shed. More trees are to be planted in addition to this.
4. To monitor air pollution, air pollution monitoring device has been installed in Harduaganj goods shed.



**Divisional Rail Manager**  
**North Central Railway, Prayagraj**

(Himansu Badoni)  
D R M / N C Railway  
Prayagraj

Work Particulars :

Proposal was Edited during Processing. Show Changes

Plan Head: 53 - Passenger Amenities (Type: Other Than Washable Apron) Priority Rank:

Short Description: Harduaganj ~ Upgradation of existing goods shed at Harduaganj as world class goods shed

Description: PRY ~ Upgradation of existing goods shed at Harduaganj as world class goods shed

Sub Head: Other Railway Users' Amenities Classification: Unclassified

Estimates	Allocation	Cost	Outlay	Department	Cost	Abstract Cost
		(in Rs. Thousands)	(in Rs. Thousands)		(in Rs. Thousands)	
	CAP	278965	0	Civil	268563	
				Electrical (G)	4230	
				Telecom	3302	

Division: Prayagraj State: UTTAR PRADESH Station/Section: Harduaganj (HGJ)

Budget Year: 2023-2024 Out of Turn: No Vetted Cost: 276095

Gauge: BG Route Class: Nature of Work: Other than Safety Related

Rail Type: Sleeper Type: Feasibility: Yes Quantity:

ROR(%): CRRM: Shortlisting Status: Shortlisted with cost 276095 with remarks: Shortlisted

Site Plan Required?: Not required

Vetting Status: Vetted by Division

Umbrella Work's details :

Process Under Umbrella Work:

Name of Umbrella Work: North Central Railway- Upgradation/Modernisation of Infrastructure at good sheds (PB#1302/NR/2023-24)

Name of Main Umbrella Work: Upgradation/Modernisation of Infrastructure at good sheds (Umbrella work 2023-24)

Railway of Umbrella Work: NCR

Sanction Year: 2023-2024

Project ID: 06.00.53.23.1.00.001

Allocation	Cost (in Rs. Ths.)	Outlay Proposed (in Rs. Ths.)	Current Outlay Alloted (in Rs. Ths.)
CAP	4658800	0	601900

DRM Priority Work Tag

Opted for expedite execution of work by initiator of proposal: -

DRM's Personal Certificate Status: - DRM Priority Works Tag: -

Gati-Shakti Tag

Proposal marked under "Gati-Shakti Tag":

Presently, about 20 rakes of clinker are unloaded every month at Harduaganj Goods Shed. There is a need to make Harduaganj goods shed world class to solve the problem of air pollution due to clinker unloading and to adopt loading unloading process as per NGT guidelines. That's why work proposal is necessary .

Justification Scope of work is as following:-

1. Provision of heavy duty warf(700m x 30m x 0.6m)
2. Proper Drainage system.(2 x 700m).
3. Approach Road RCC-1800 m
4. Merchant room+Toilet+Bathroom(5m X 5m), Labor room+ Toilet+ Bathroom (5m X 15m), CGS room+ TMS Room+Toilet(5m x 7m)
5. Boundary wall-700 m
6. Earth filling - 14700 cubic m
7. High Mast Tower-02 Nos.
8. Track work for full operation( 750m from 360m)
9. Provision of CCTVs for monitoring loading & unloading areas

Hence, the work is essentially required so the work may get proposed.

Files Attached:

S.No.	Subject	FileName	File Type
1	sketch pain og HGJ goods shed	Sketch plan of Harduaganj Goods Shed.pdf	Detailed Scope
2	Cost of civil work at HGJ	civil eng cost of HGJ.pdf	Detailed Scope
3	Cost of Electrical G	cost of Electrical G.pdf	Detailed Scope
4	FINACIAL JUSTIFICATION OF HGJ	financial justification of HGJ.pdf	Detailed Scope
5	Lertter for compliance of NGT	Letter for comply NGT order.pdf	Detailed Scope
6	Cost of Telcom work	S&T cost.pdf	Detailed Scope
7	ROR OF HGJ	ROR PF HGJ.xlsx	Detailed Scope
8	2023/GS/SD-1/08/14/NCR(2023-24	NCR Prayagraj sanctioned works dated 31.08.2023.pdf	Sanction Letter

Download all Attachments

View Other Attachments

Noting

View Full Screen

(Himansu Badoni)  
D.R.M./N C. Railway  
Prayagraj

333

May please attach GSU tag as per discussion with CA.

SDCMALD  
27/06/2023 11:43:47



(Himansu Badoni)  
D.R.M./N.C. Railway  
Prayagraj

# Boundary wall with sheet covering



*H*  
(Himansu Badoni)  
D R M / N C Railway  
Prayagraj

402

757

# Track work has been completed



(Himansu Radoni)  
D R M / N C Railway  
Jayagraj

758

401

# Heavy duty wharf work along line no. 15




(Himansu Badoni)  
D.R M/N C Railway  
Prayagraj



**Aligarh, Uttar Pradesh, India**  
**X4qf+m65, Aligarh, Uttar Pradesh 202127, India**  
**Lat 27.988917° Long 78.126191°**  
**10/03/2025 01:56 PM GMT +05:30**

Plantation alongwith boundary wall

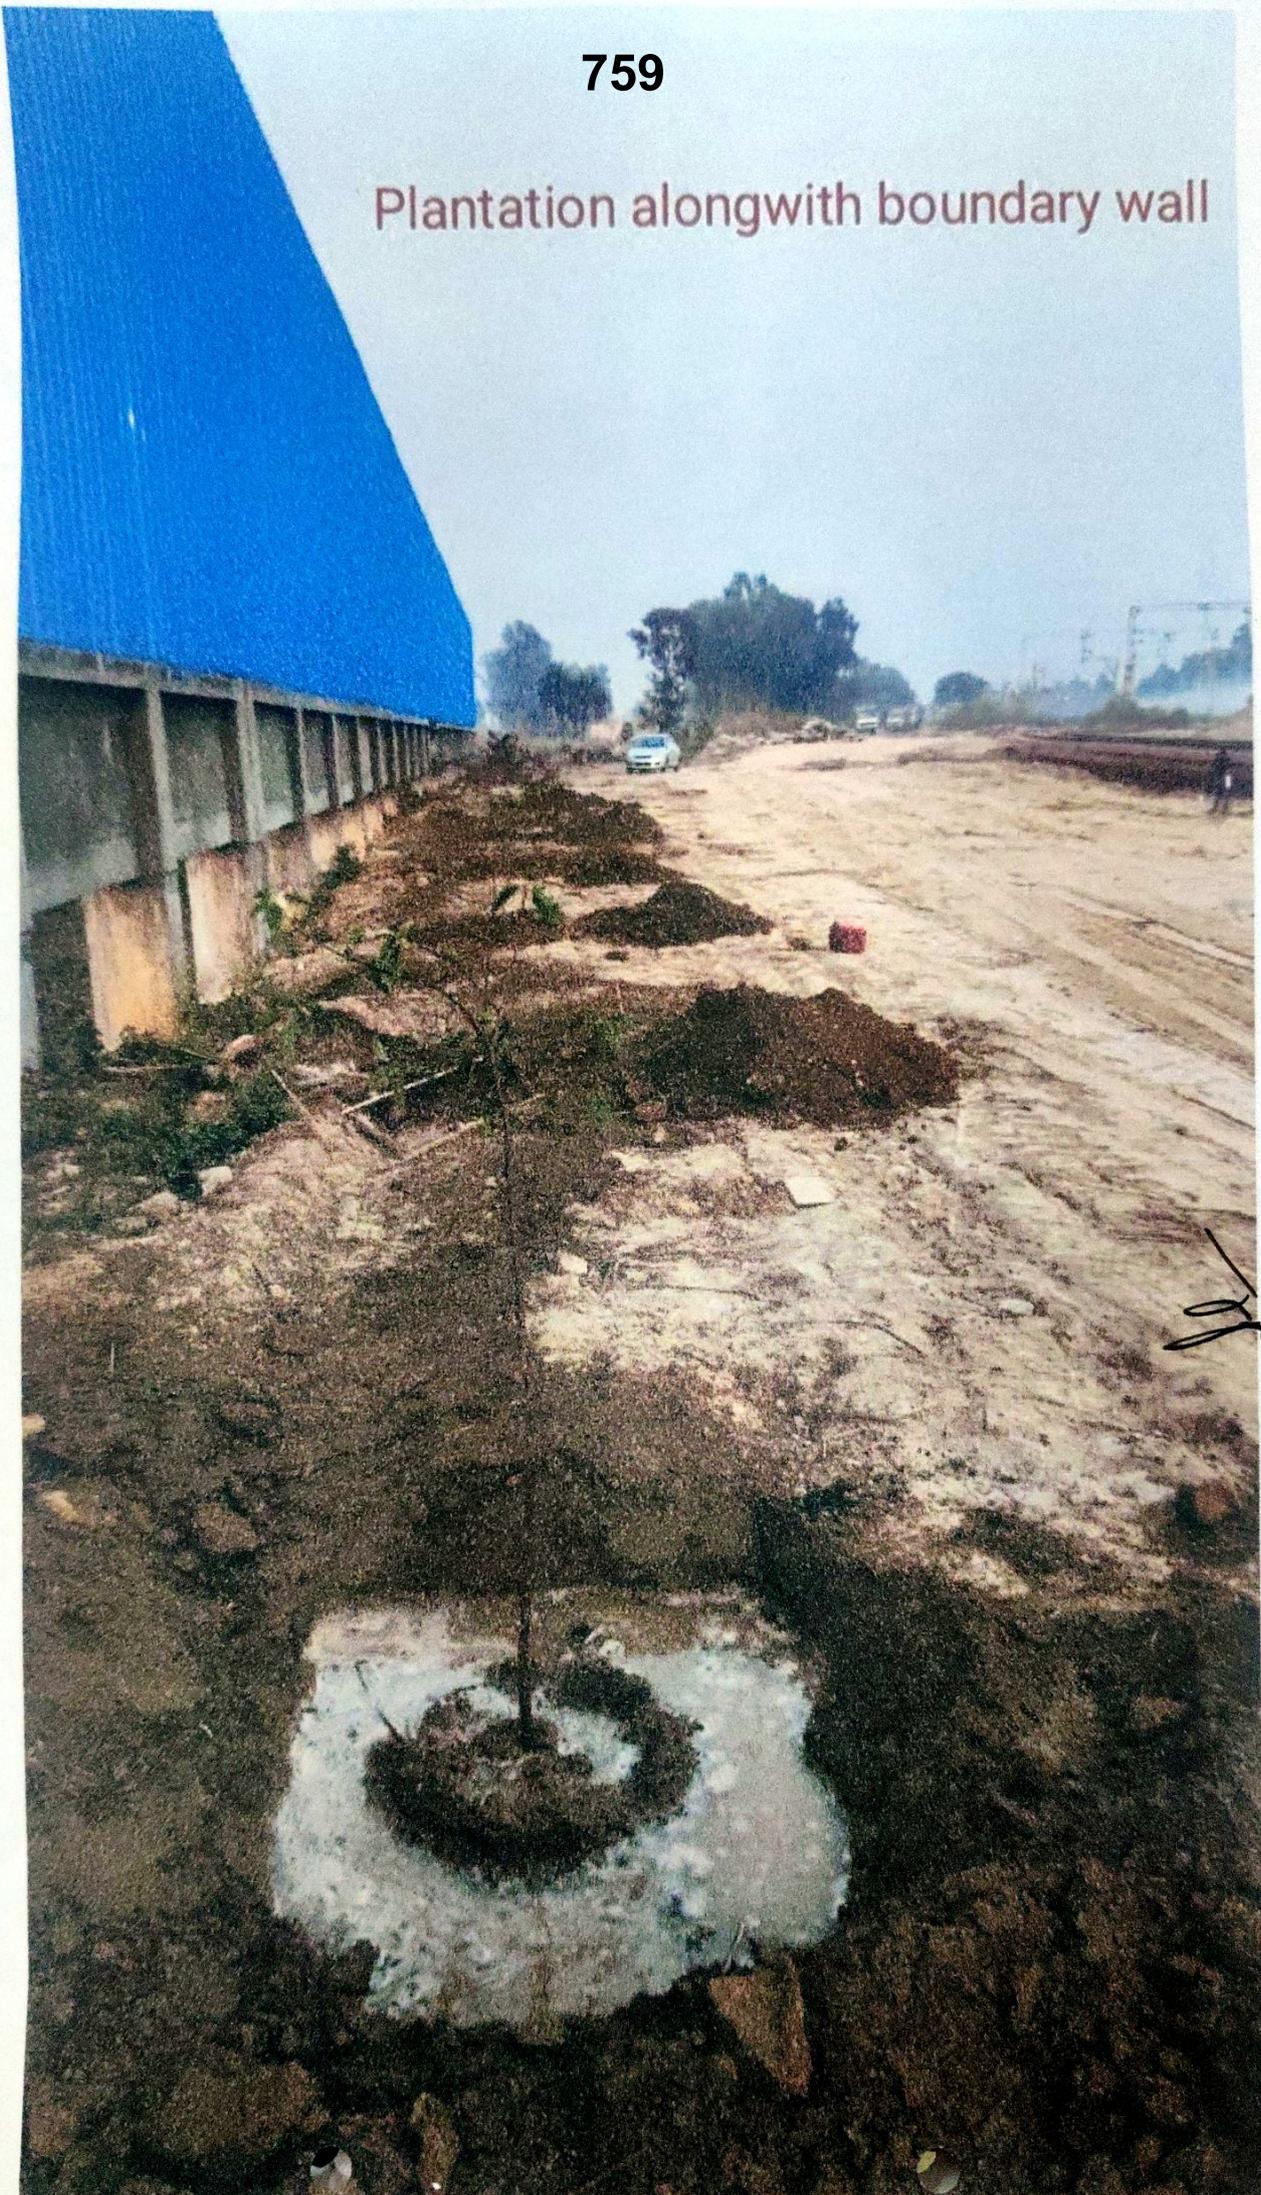

(Himansu Badoni)  
D.E.M./N.C. Railway  
yagraj

760

Water sprinkling at unpaved Approach road

  
(Himanshu ...)  
Q.R.M. Railway  
...
