

**BEFORE THE NATIONAL GREEN TRIBUNAL
PRINCIPAL BENCH, NEW DELHI**

ORIGINAL APPLICATION NO. 274/2022

IN THE MATTER OF:

PREM AGGARWAL & ORS.

...APPLICANT(s)

VERSUS

GOVERNMENT OF NCT OF DELHI


...RESPONDENT(s)

INDEX

S. NO.	PARTICULARS	PAGE NO.
1.	UPDATED PROGRESS REPORT BY WAY OF AFFIDAVIT ON BEHALF OF THE RESPONDENT NO. 8, U.P. JAL NIGAM (URBAN), STATE OF U.P.	
2.	A COPY OF THE MAP OF THE SAHIBABAD DRAIN AND THE DRONE VIDEO IS ANNEXED HEREWITH AND MARKED AS ANNEXURE-1	
3.	A COPY OF THE REPORT SHOWING THE CONSTRUCTION PROGRESS ALONGWITH THE PHOTOGRAPHS IS ANNEXED HEREWITH AND MARKED AS ANNEXURE-2	
4.	A COPY OF THE MAP OF THE DRAINS IS ANNEXED HEREWITH AND MARKED AS ANNEXURE-3	
5.	A COPY OF LETTER DATED 12.03.2026 IS ANNEXED HEREWITH AND MARKED AS	

	ANNEXURE-4	
--	------------	--

THROUGH COUNSEL



BHANWAR PAL SINGH JADON
COUNSEL FOR RESPONDENT NO. 8
bhanwar09jadon@gmail.com | 6375115224

DATE: 29.04.2026

PLACE: NOIDA

**BEFORE THE NATIONAL GREEN TRIBUNAL
PRINCIPAL BENCH, NEW DELHI
ORIGINAL APPLICATION NO. 274/2022**

IN THE MATTER OF:

PREM AGGARWAL & ORS.

...APPLICANT(s)

VERSUS

GOVERNMENT OF NCT OF DELHI


...RESPONDENT(s)

**UPDATED PROGRESS REPORT BY WAY OF AFFIDAVIT ON BEHALF
OF THE RESPONDENT NO. 8, U.P. JAL NIGAM (URBAN), STATE OF
U.P.**

I, Arun Pratap Singh, aged about 35 years, S/o Shri Yarendra Pal Singh,
posted as Executive Engineer, do hereby solemnly affirm and state
as under:

1. That I, the Deponent, am fully conversant with the facts of the case and am competent and authorized to swear the present Affidavit.
2. That in the present matter, the applicants have raised grievances regarding discharge of untreated sewage, industrial waste in the storm water drain,

29 APR 2026




stagnation of drain with floating plastic waste and causing of environmental pollution by the gases emitted.

3. **BACKGROUND**

- i. That the discharge of the Sahibabad Drain (length measuring about 12.73 kms) starting from Bhopura ward of Ghaziabad Nagar Nigam, before meeting with the Shahdara drain near Ghazipur Dumping Yard, Delhi. The drain was intercepted near NH-24 and diverted to the operational 74 MLD STP at Indirapuram for treatment in 2013. The discharge was recorded as 90 MLD in the year 2019.

A copy of the map of the Sahibabad drain is annexed herewith and marked as **ANNEXURE-1**.

- ii. That to mitigate the issue of overflow at the STP, a 17 MLD SPS (Sewage Pumping Station) at Shalimar was commissioned in 2020. The excess sewage through the aforementioned SPS is diverted to the operational 56 MLD STP at Indirapuram for treatment.



29 APR 2026

4. **PROBLEMS/ISSUES**


That, however, recent observations revealed an overflow at the interception point, which is attributed to two primary factors:

- i. damage of 220m in trunk sewer line in Brij Vihar, resulting in the overflow of approximately 15 MLD
- ii. Increased wastewater flow, by 12 MLD, from developed residential areas located near north of Ghaziabad- Wazirabad Road. The increased wastewater flow is domestic sewage of Gagan Vihar, Bhopura and Kuti residential area, located in North of Ghaziabad- Wazirabad Road.

5. **REMEDIAL ACTIONS BEING TAKEN AND CURRENT PROGRESS**

i. **GHAZIABAD SEWERAGE SCHEME (KARHERA ZONE):**

- a. That the above-mentioned scheme has been sanctioned under the AMRUT 2.0 Programme introduced by the Union of India.
- b. That under this project, the construction of the 68 MLD STP, a Main Pumping Station (MPS), 03 nos. of Intermediate Pumping Stations (IPS), and laying of 155 km of sewer network, along with the provision of the 67,669 house sewer connections



29 APR 2026


which includes residential area North of Ghaziabad- Wazirabad Road is under progress.

- c. That the above-mentioned 68 MLD STP construction will reduce the discharge of the Sahibabad drain by 12 MLD.
- d. That the construction work commenced on 11.12.2023 and the **current physical progress of the scheme, as of date, stands at 82.22% and the balance works shall be completed by June, 2026.**
- e. **That the construction of 68 MLD STP, MPS and IPS at Arthala has been completed and made operational.**

A copy of the report showing the construction progress along with the photographs is annexed herewith and marked as **ANNEXURE-2.**

ii. **REPLACEMENT OF DAMAGED TRUNK SEWER LINE CONNECTED TO 56 MLD STP INDIRAPURAM (SBR):**

That the Crown of Trunk sewer at 02 locations (1400mm dia. trunk sewer in Brij Vihar area, and 1800 mm dia. trunk sewer in Indirapuram, downstream of Brij Vihar) was damaged, which led to the overflow of 15 MLD sewage into the Sahibabad Drain from the



29 APR 2026

damaged portion. To curb the overflow of 15 MLD due to damage to trunk sewer line, **the work of replacement of damaged 1400 mm dia. and 1800 mm dia. trunk sewer line has been executed by the Jal Kal, Nagar Nigam, Ghaziabad under OCOP Contract and the work by the agency has been duly completed, report from the Ngar Nigam Ghaziabad is awaited.**

iii. **INDIRAPURI DRAIN AND BANTHLA DRAIN:**


a. That it is humbly submitted before the Hon'ble Tribunal that the above-mentioned drains carry untreated sewage of about 85 MLD, Indirapuri (65 MLD) and Banthla (20 MLD).

A copy of the map of the drains is annexed herewith and marked as **ANNEXURE-3**.

b. That the preparation of the DPR for the I&D works is under progress.

c. That the said DPR is being prepared for the treatment of sewage of Indrapuri drain (65 MLD), Banthala Drain (20 MLD) and Lalbag Loni drain (15 MLD).

d. That furthermore, it has been informed by the Nagar Palika Parishad, Loni vide letter dated 12.03.2026 to the UP Jal Nigam



29 APR 2026

(Urban) that the land for construction of the STP has been allotted at Khasra No. 346/3,4 in Sadullabad, Ghaziabad having a total area of 4.7540 ha.


A copy of letter dated 12.03.2026 is annexed herewith and marked as **ANNEXURE-4**.

- e. That the said DPR shall be prepared and submitted to the NMCG through the SMCG by 31.05.2026. Subsequent to the approval of the DPR, the works will require a period of 30 months from the date of start.

iv. DLF ANKUR VIHAR, LONI:

- a) That the present drain carrying the sewage of approximately 04 MLD will be tapped at 30 MLD existing STP at Loni under the Loni Sewerage Scheme Phase 3 part 1, sanctioned under Amrut 2.0 Programme. It is submitted that the project is likely to be completed by **JULY, 2026**.

6. Hence, the present affidavit is being filed for the kind consideration and perusal of this Hon'ble Tribunal.



29 APR 2026

7. I state that everything stated above has been stated by me in my official capacity on and derived from the official records and I state that nothing material has been concealed therefrom.





DEPONENT

VERIFICATION

Verified at Ghaziabad on this 29th day of APRIL, 2026, that the contents of the above affidavit from paragraphs 1 to 7 are believed to be true and correct to the best of my knowledge and belief. No part of it is false and nothing material has been concealed therefrom.



DEPONENT




ATTESTED
29 APR 2026

PRAMOD KUMAR SHARMA
Notary Public
Ghaziabad (U.P.) INDIA

DRAIN MAP OF NAGAR NIGAM GHAZIABAD

ANNEXURE-1

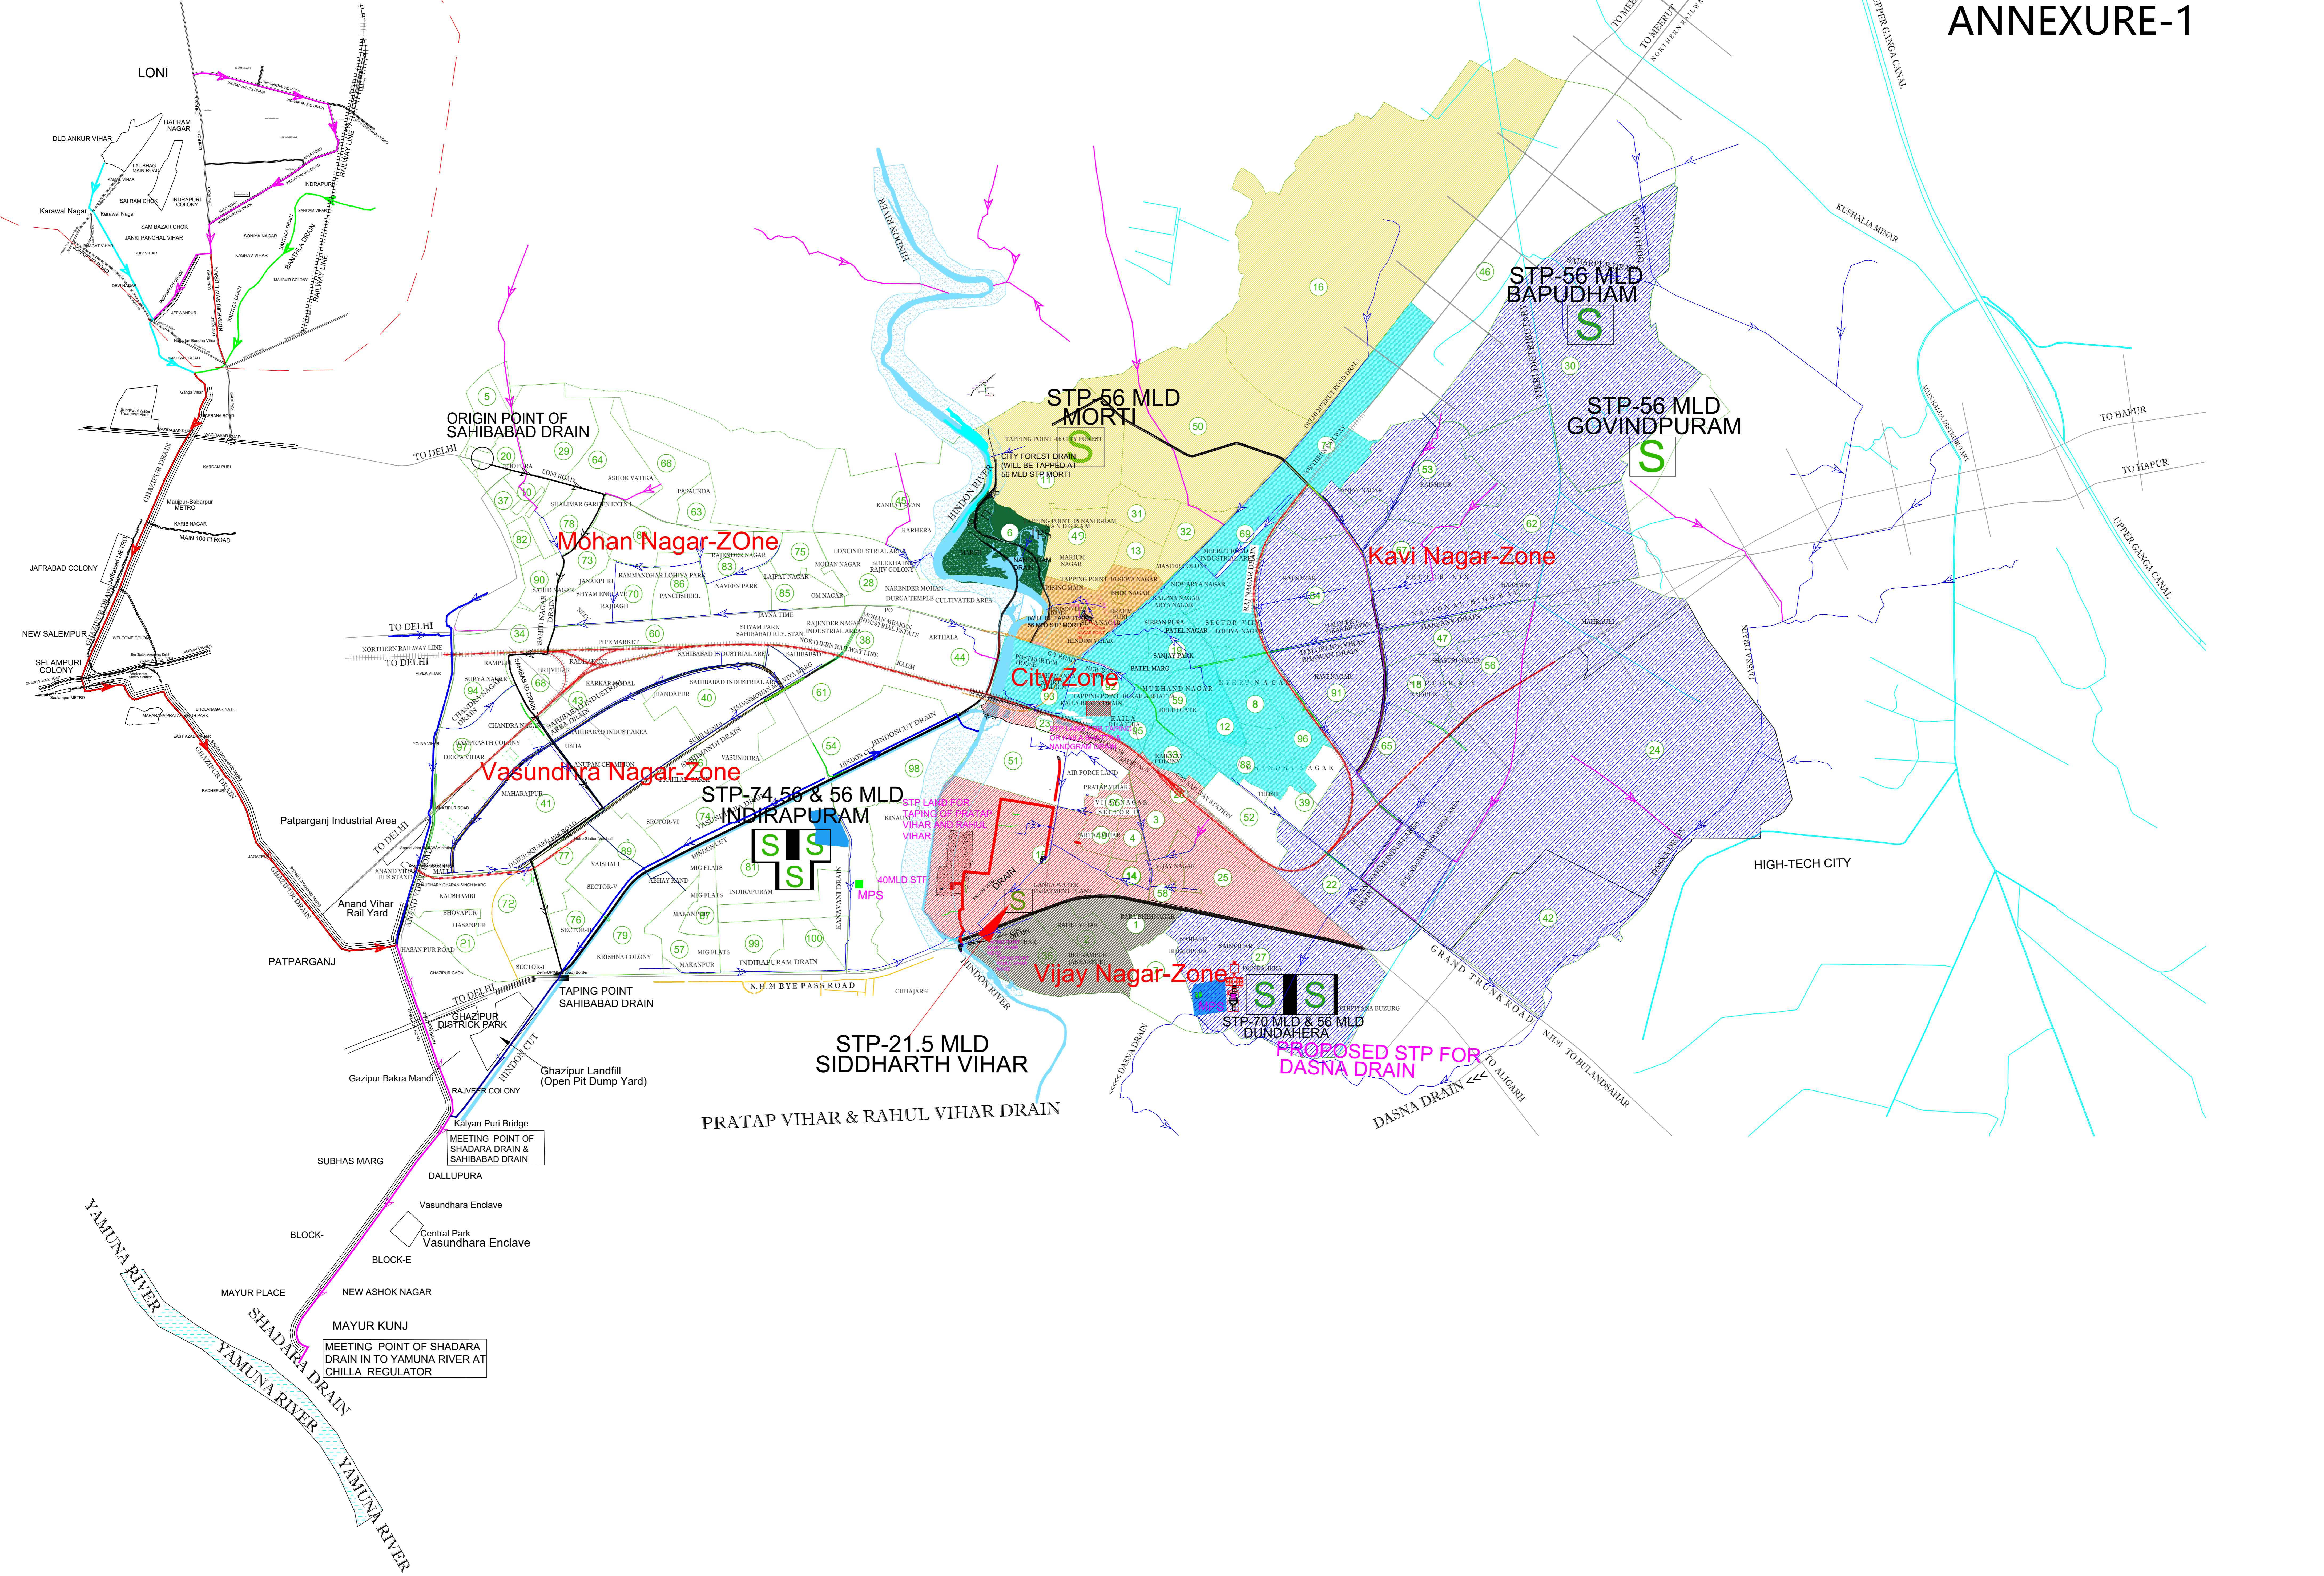

Zone)

ANNEXURE-2

S.No	Description	Qty	progress	Remark
1	STP (68 MLD)	1 No	100%	Trial & Run in progress
2	Main Pumping Station	1 No	100%	Trial & run in progress
3	Sewer Network	155 km	151 km	Work in progress
4	Sewer House Connection	67669 No	4000 No.	Work in progress
5	IPS Arthala	1 No.	100%	Trial & run in progress
6	IPS Bhopura	1 No.	85%	Work in progress
7	IPS Pasonda	1 No.	75%	Work in progress

68 MLD STP has been commissioned. Overall physical progress of the scheme is 85%. Likely completion date of the project is June, 2026.

Photograph of 68 MLD STP Karhera



Photograph of Main Pumping Station





Photograph of Staff Quarter





Photograph of sewer laying and road restoration






Photograph of IPS Arthala






Photograph of IPS Bhopura

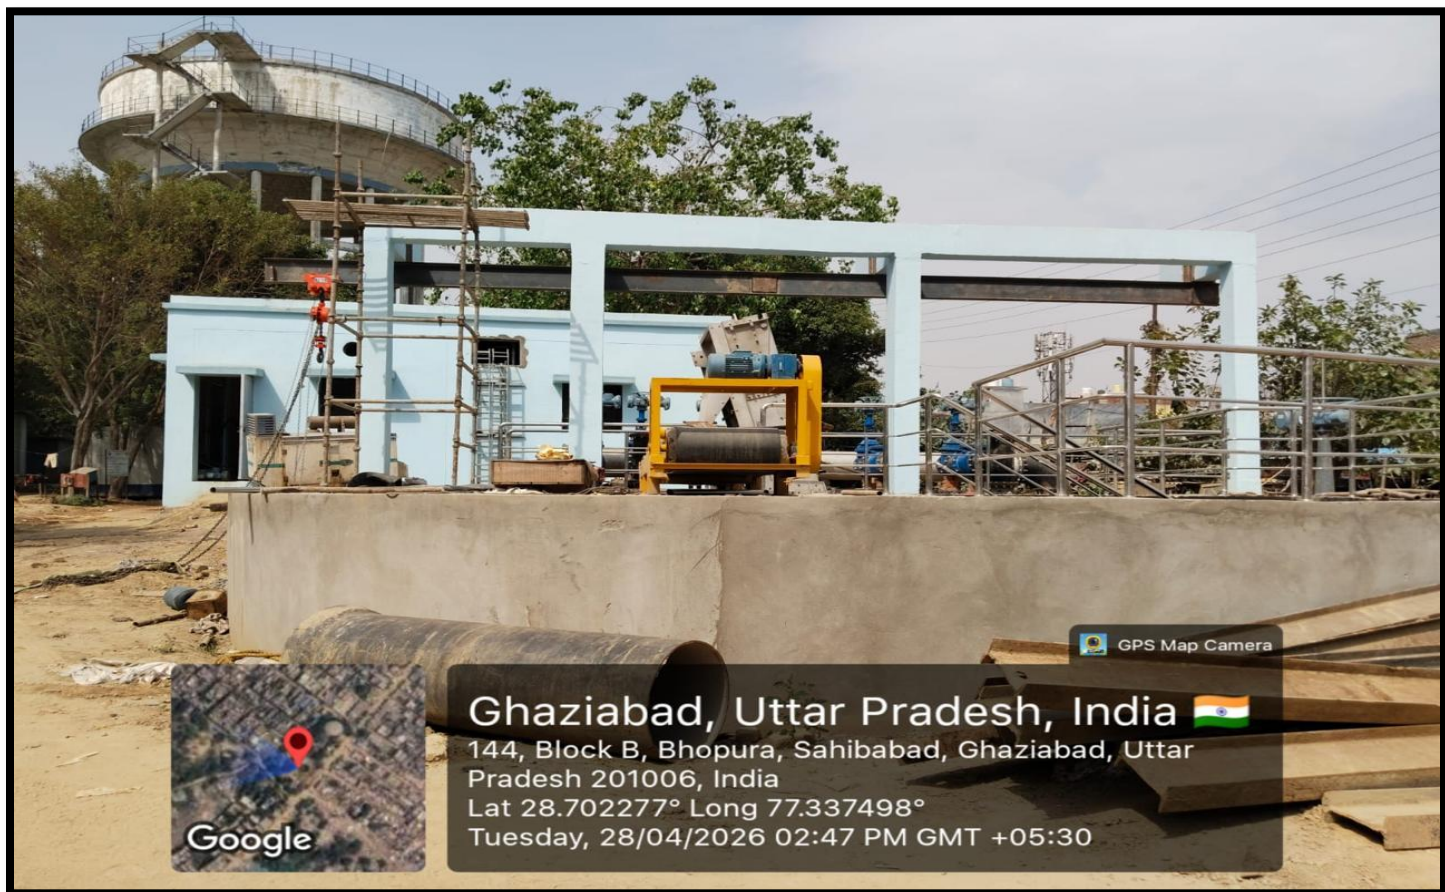




Photograph of IPS Pasonda





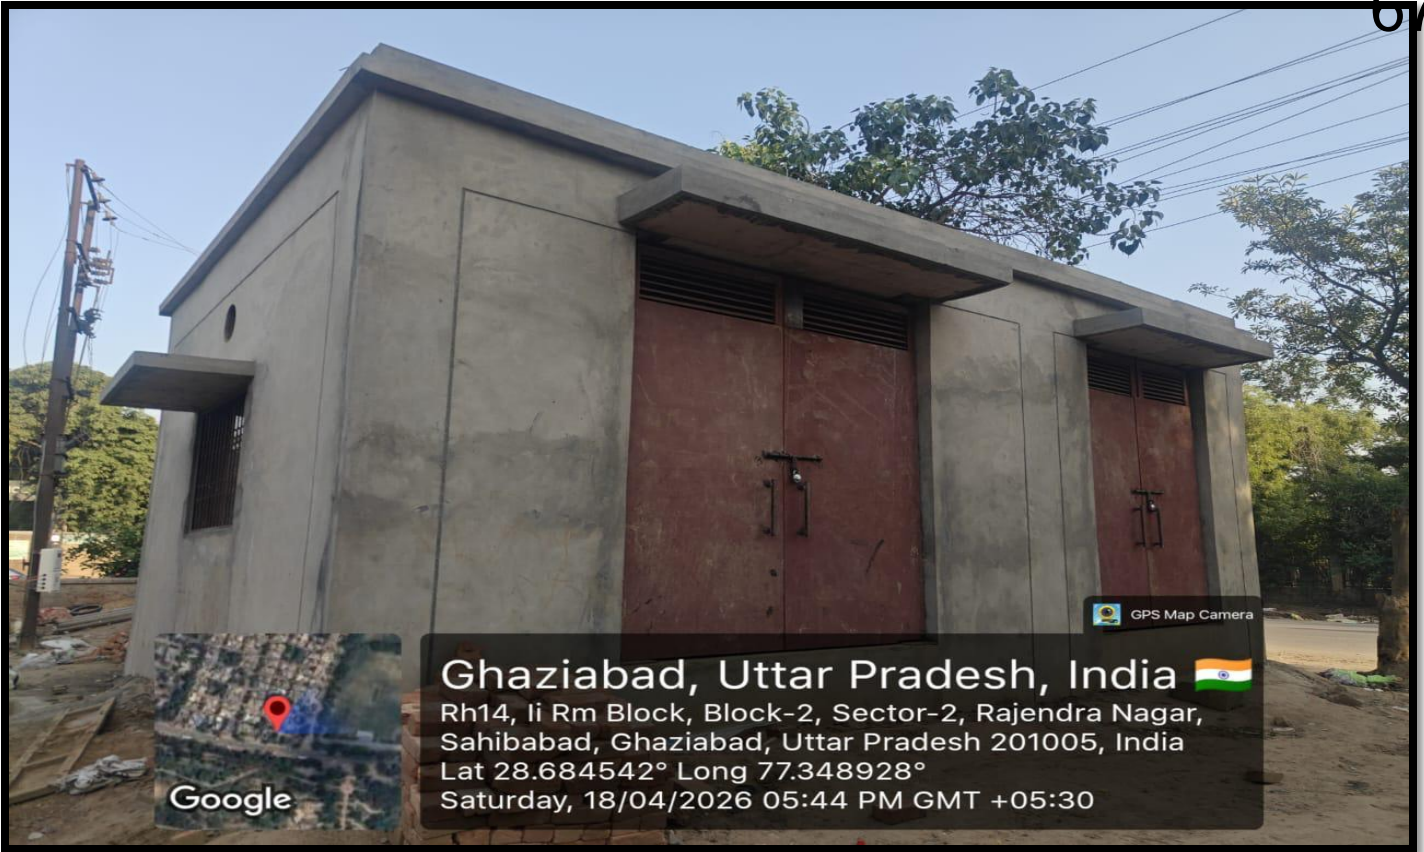

Photographs of sewer house connection

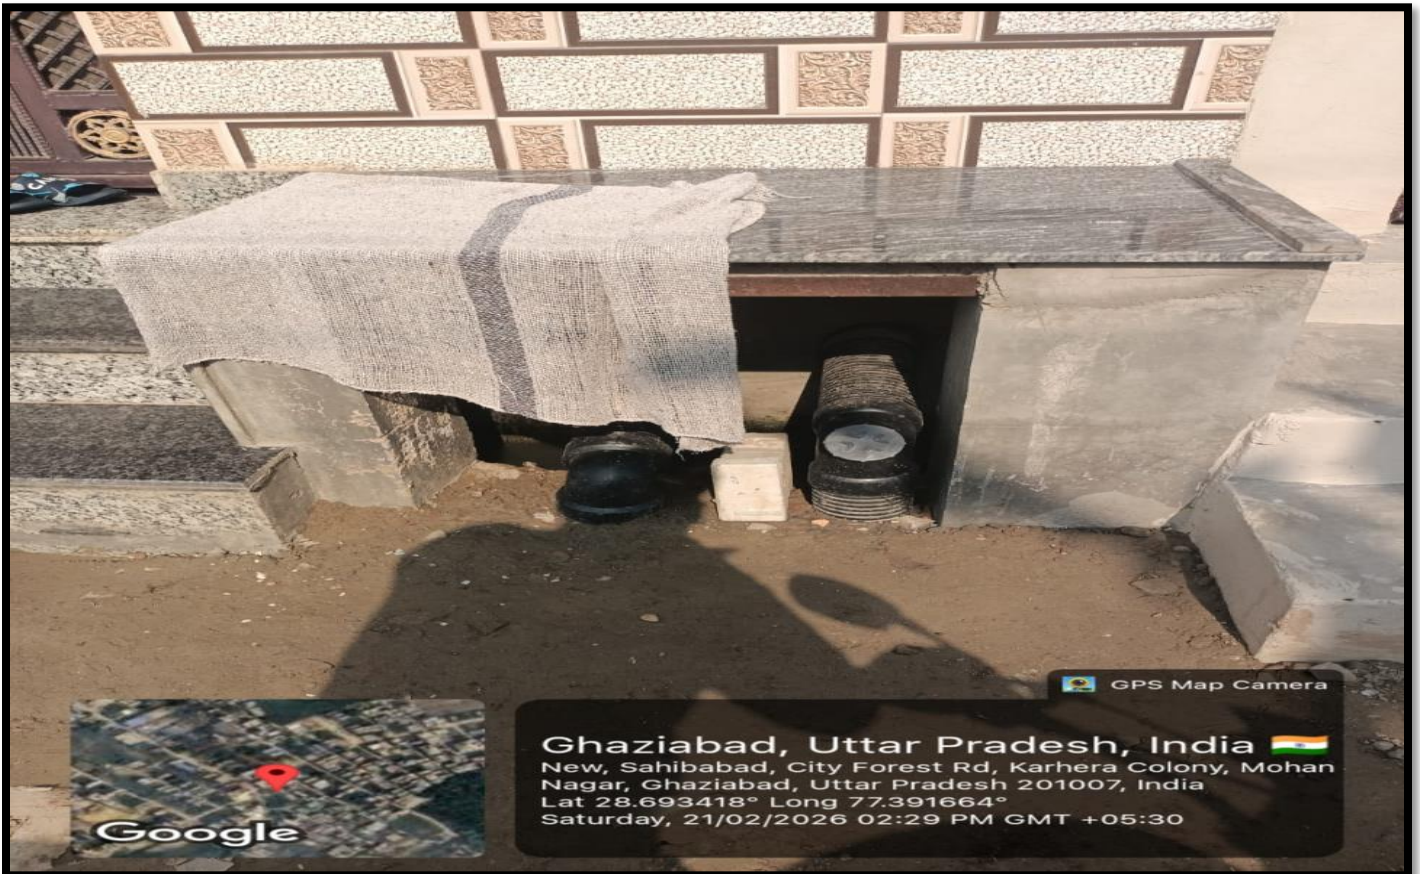

671

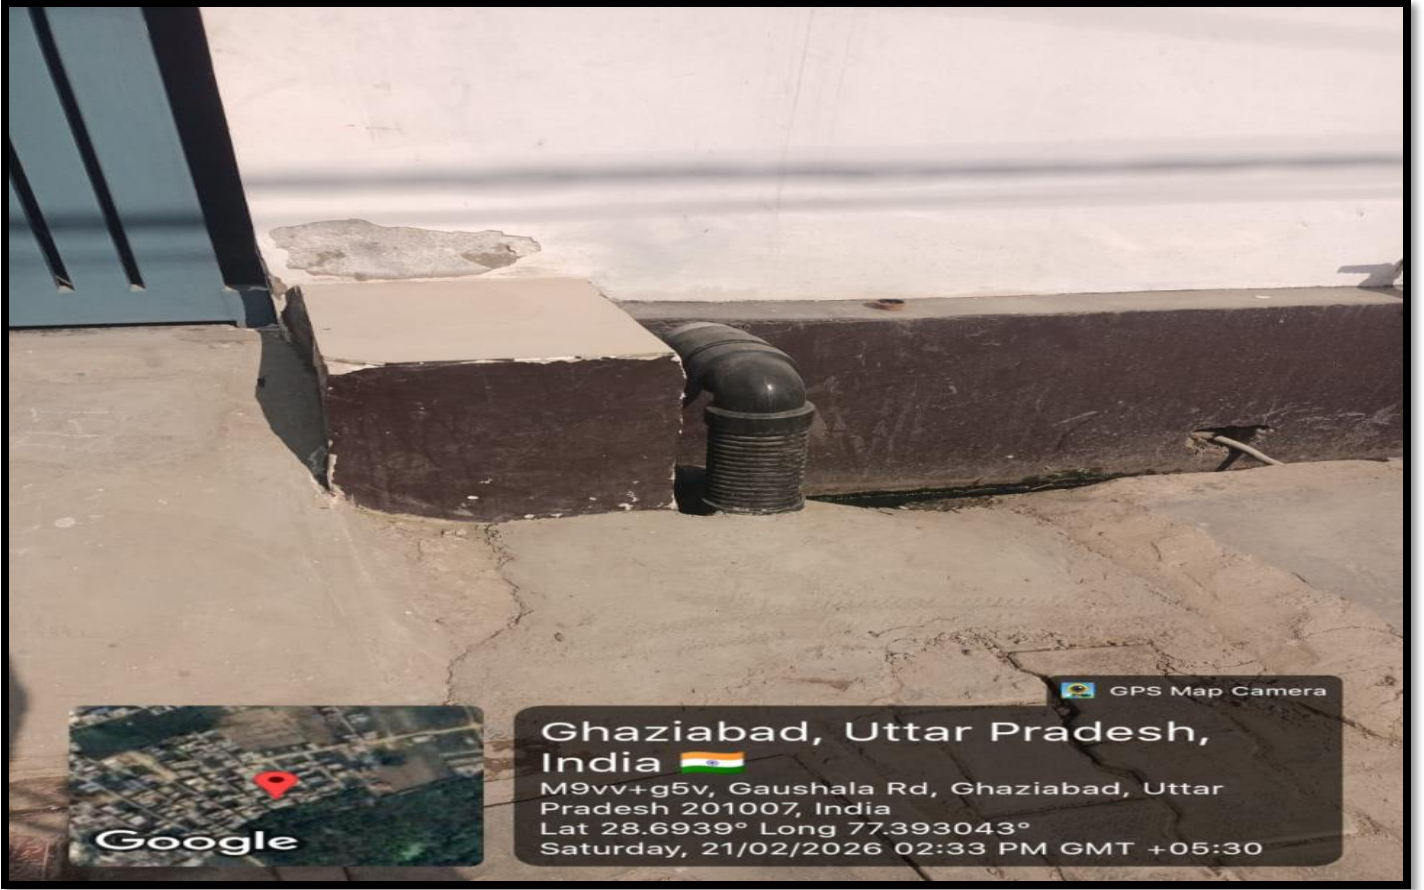

Ghaziabad, Uttar Pradesh,
India 🇮🇳


M9vv+g5v, Gaushala Rd, Ghaziabad, Uttar
Pradesh 201007, India

Lat 28.6939° Long 77.393043°

Saturday, 21/02/2026 02:33 PM GMT +05:30

GPS Map Camera

MAP SHOWING DRAINS CONTRIBUTING FLOW IN SHAHDARA DRAIN

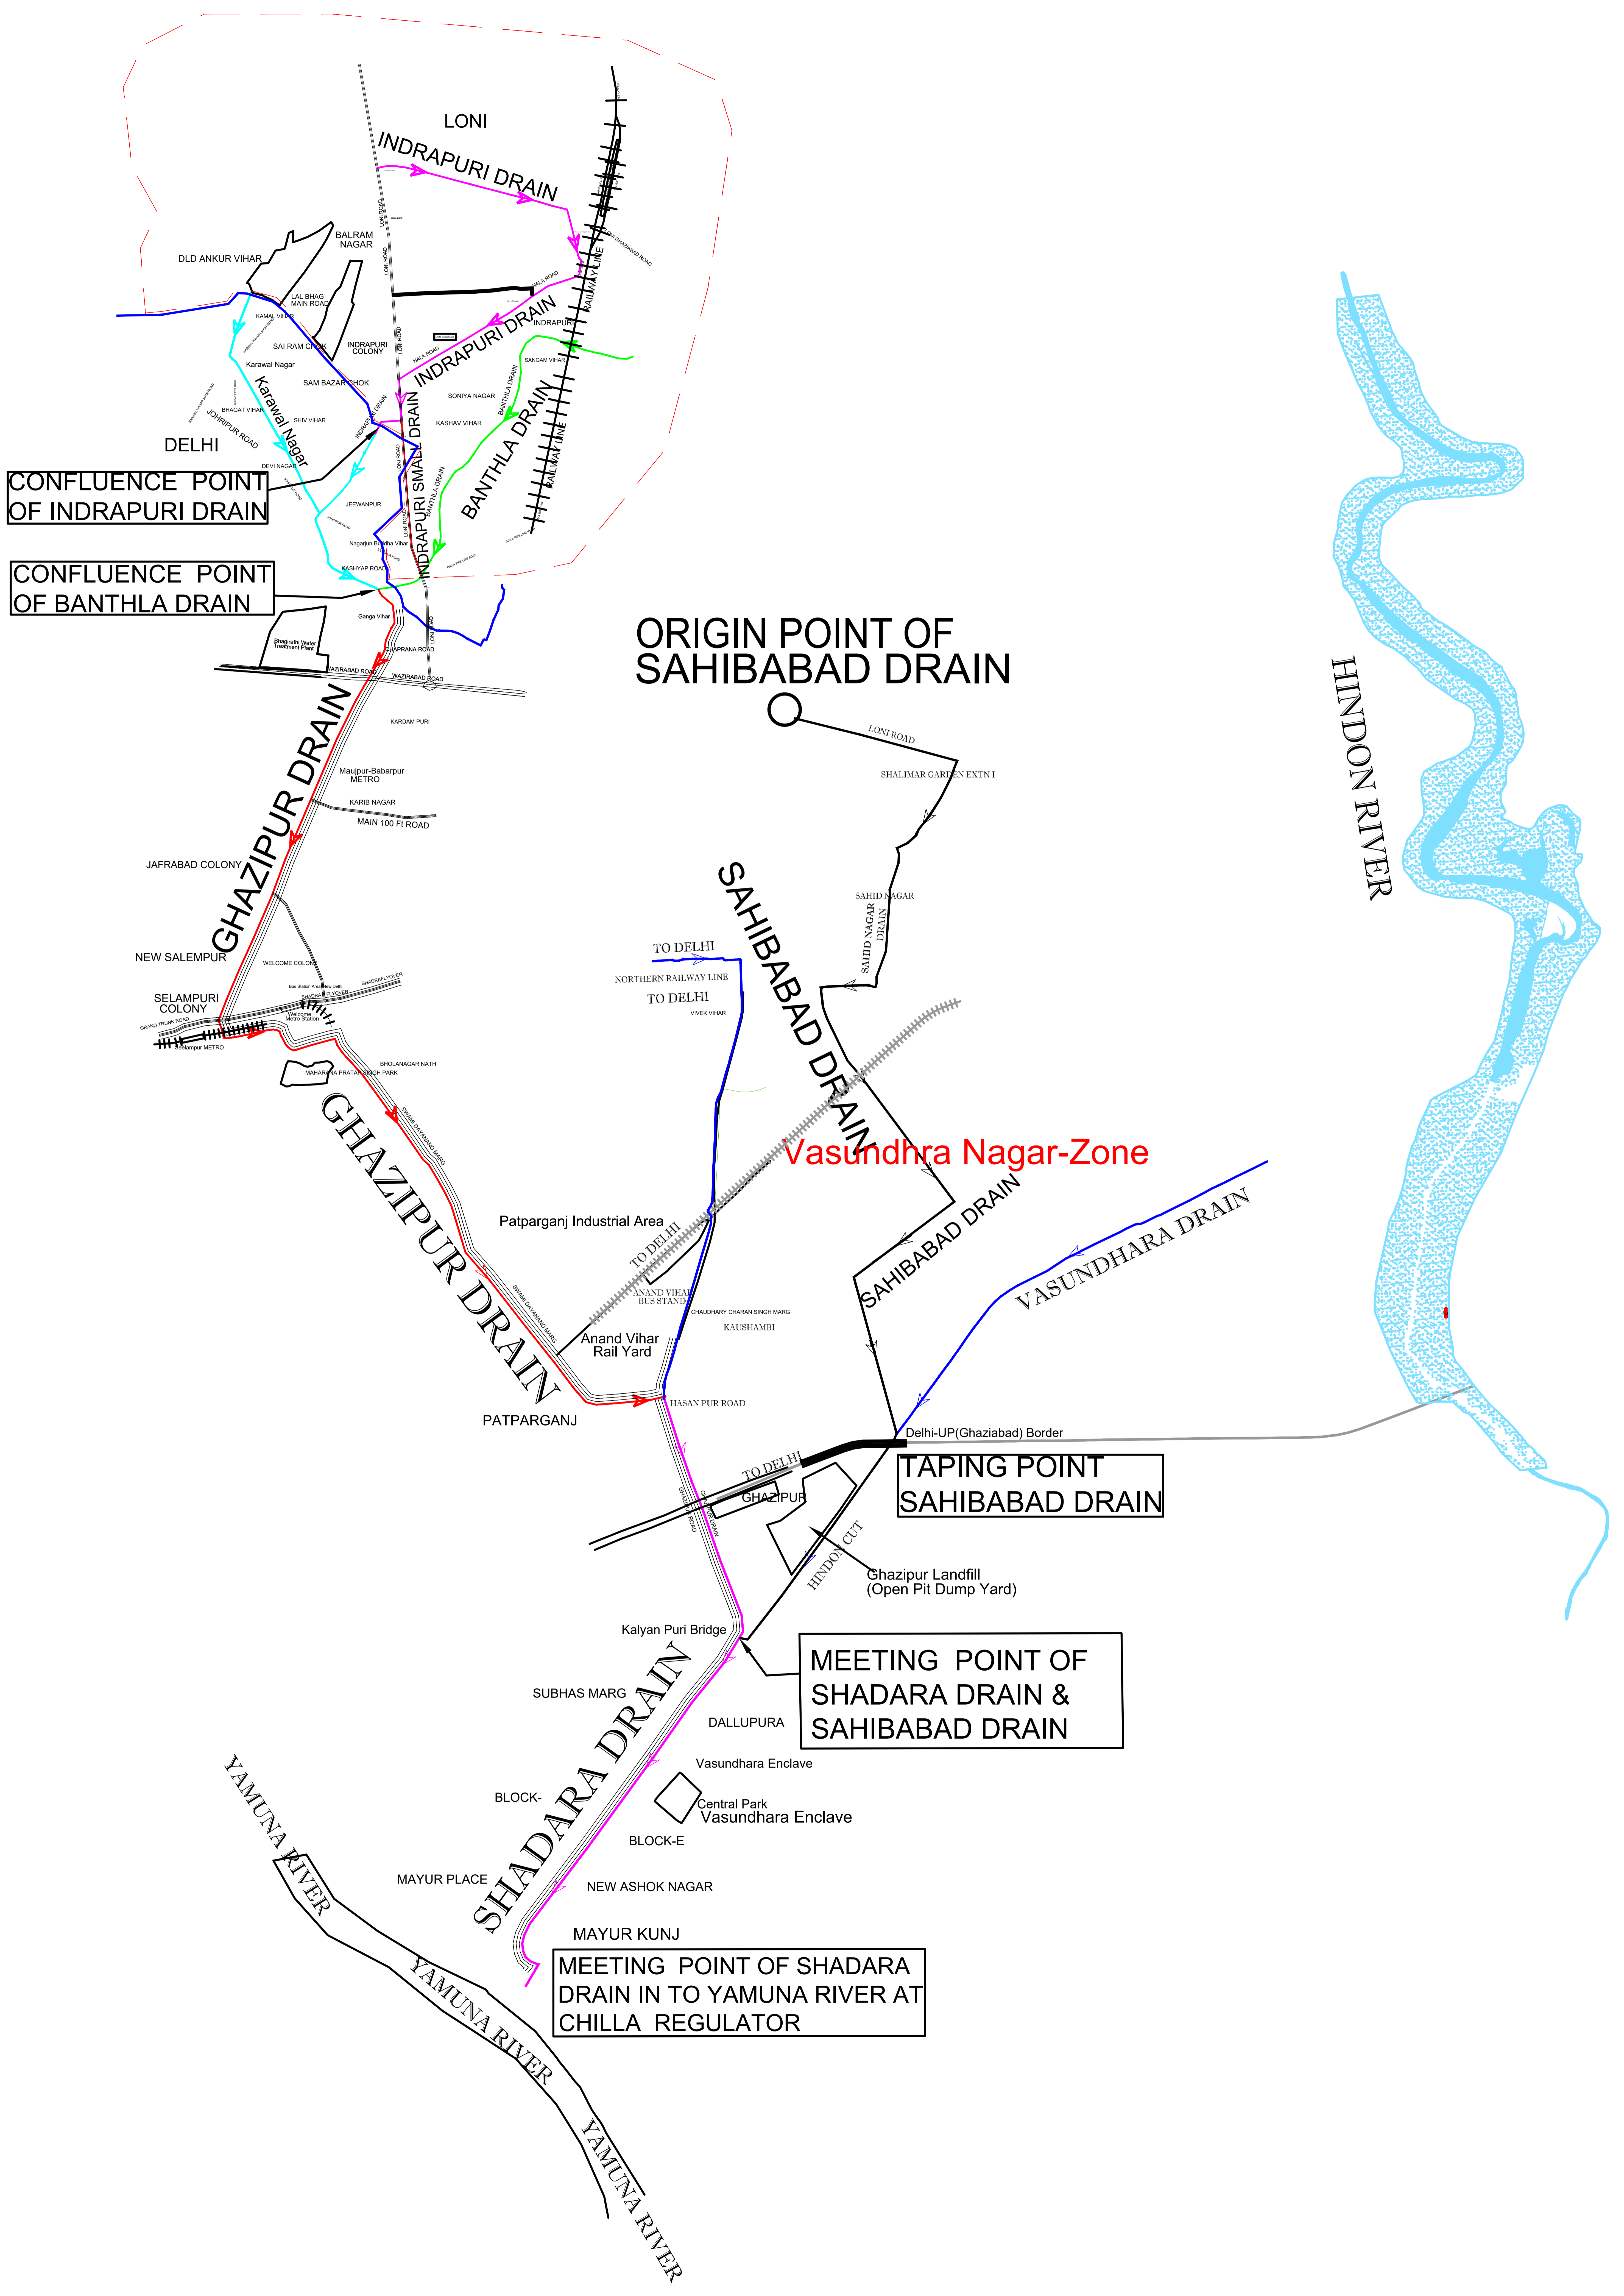

कार्यालय नगर पालिका परिषद लोनी गाजियाबाद

पत्रांक सं०-२१५ / न०पा०परि०-लोनी / 2025-26

दिनांक-12 मार्च, 2026

सेवा में,

ANNEXURE-4

अधिसासी अभियन्ता

निर्माण खण्ड (प्रथम), उ०प्र० जल निगम (नगरीय)

सी-9, सै०-1, आर०डी०सी०, राजनगर, गाजियाबाद-201001

विषय:-नगर पालिका परिषद लोनी क्षेत्र के यमुना नदी में निस्तारित हो रहे 2 नग नालों (इन्द्रापुरी एवं बन्थला ड्रेन) की आई० एण्ड डी० की डी०पी०आर० के सम्बन्ध में।

महोदय,

कृपया उपरोक्त विषयक आपके कार्यालय पत्रांक-233/कार्य-20/11 दिनांक 25.02.2026 का संदर्भ ग्रहण करने का कष्ट करे, इस सम्बन्ध में आपके पूर्व पत्रांक-132/कार्य-20/06 दिनांक 05.02.2026 द्वारा नगर पालिका परिषद क्षेत्र के यमुना नदी में निस्तारित हो रहे 03 नग नालों की आई० एण्ड डी० एवं एस०टी०पी० निर्माण सम्बन्धी कार्यों की डी०पी०आर० विरचन भूमि उपलब्ध कराने हेतु अनुरोध किया गया था।

उक्त के क्रम में अवगत कराना है, कि आप द्वारा एस०टी०पी० निर्माण सम्बन्धी कार्य की डी०पी०आर० विरचन हेतु क०सं०-01 व 04 के लिये भूमि का विवरण निम्नवत् है:-

क०सं०	विवरण	ग्राम का नाम	गाटा संख्या	कुल क्षेत्रफल	एस०टी०पी० निर्माण हेतु भूमि की मात्रा	स्थल
1	65 एम०एल०डी० (प्रारम्भिक अनुमानित) एस०टी०पी०	सादुल्लाबाद	346/3,4	4.7540 हैक्टेयर	20000 वर्ग मी०	उपरोक्त खसरा नम्बर में से 5000 वर्ग मीटर भूमि गौशाला/एम०आर०एफ० सेंटर के रूप में आरक्षित की गयी है, शेष भूमि उक्त कार्य हेतु उपयुक्त है।
4	55 एम०एल०डी० एस०टी०पी० व एम०पी०एस० (प्रारम्भिक अनुमानित)				20000 वर्ग मी०	

सूचना सादर प्रेषित।

(कृष्ण कान्त मिश्र)
अधिसासी अधिकारी
नगर पालिका परिषद लोनी
गाजियाबाद

पत्रांक एवं दिनांक तदैव:-

प्रतिलिपि:- निम्नलिखित को सूचनार्थ सादर प्रेषित।

1-जिलाधिकारी महोदय, गाजियाबाद।

2-मुख्य अभियन्ता (गा० क्षेत्र), महोदय, उ०प्र० जल निगम(नगरीय), गाजियाबाद।

3-अधीक्षण अभियन्ता महोदय, निर्माण मण्डल, उ०प्र० जल निगम (नगरीय), गाजियाबाद।

अधिसासी अधिकारी
नगर पालिका परिषद लोनी
गाजियाबाद
